



QAD Enterprise Applications
Standard & Enterprise Edition

Training Guide Master Scheduling and RCCP

70-3036B
QAD 2010 Standard & Enterprise Edition
Lab: Enterprise Edition 2010 - Addons r03 - Training
Workspace: 10USA > 10USACO
October 2010

This document contains proprietary information that is protected by copyright and other intellectual property laws. No part of this document may be reproduced, translated, or modified without the prior written consent of QAD Inc. The information contained in this document is subject to change without notice.

QAD Inc. provides this material as is and makes no warranty of any kind, expressed or implied, including, but not limited to, the implied warranties of merchantability and fitness for a particular purpose. QAD Inc. shall not be liable for errors contained herein or for incidental or consequential damages (including lost profits) in connection with the furnishing, performance, or use of this material whether based on warranty, contract, or other legal theory.

QAD and MFG/PRO are registered trademarks of QAD Inc. The QAD logo is a trademark of QAD Inc.

Designations used by other companies to distinguish their products are often claimed as trademarks. In this document, the product names appear in initial capital or all capital letters. Contact the appropriate companies for more information regarding trademarks and registration.

Copyright ©2010 by QAD Inc.

MasterScheduling_TG_v2010EE.pdf/lkk/hes

QAD Inc.

100 Innovation Place
Santa Barbara, California 93108
Phone (805) 566-6000
<http://www.qad.com>

Contents

About This Course	1
Course Description	2
Course Objectives	2
Audience	2
Prerequisites	2
Course Credit and Scheduling	2
Virtual Environment Information	2
QAD Web Resources	3
Chapter 1 Introduction to Master Scheduling and RCCP	5
Course Overview	6
Planning and Scheduling Overview	7
Planning Levels Supported by QAD Enterprise Applications	8
Product Line and Resource Planning	8
End-Item Planning	8
Component Planning	9
Enterprise Resource Planning (ERP)	9
Planning and Scheduling Phases	10
Planning and Scheduling Areas of Concern	14
Master Schedule	14
Rough-Cut Capacity Planning (RCCP)	14
RCCP Compared to CRP	15
Statement of Production	16
Benefits of a Master Schedule	17
Terminology	19
Rough-Cut Capacity Planning (RCCP)	21
Master Schedule and RCCP Uses	22
Course Objectives	23
Chapter 2 Business Considerations	25
Course Overview	26
Business Considerations	27
Planning Overview	28
Items to Master Schedule	30

Multilevel Master Schedule	32
Production Forecast in QAD Enterprise Applications	33
Determine What Resources Need RCCP	35
Seasonal Build Requirements	36
MRP Horizon	37
Time Fence	39
Features and Options	41
Production Constraints	42
Summary	44

Chapter 3 Set Up Master Scheduling and RCCP45

Course Overview	46
Simulated Forecasting	47
Balance Demand and Supply	48
Item and Item-Site Planning Maintenance	50
Identify Master Scheduled Items	51
Item Planning Maintenance	52
Item-Site Planning Maintenance	58
Approaches to Master Scheduling	59
Computer Assisted Approach (Recommended)	60
Fully Automatic Approach	62
Fully Manual Approach	63
Multilevel Master Scheduling	64
Planning Bills	65
Top-Level Items	66
Family-Level Item Values	66
MRP Control	68
Holiday/Calendar Maintenance	70
Calendar Maintenance	71
Holiday Maintenance	73
Rough-Cut Capacity Planning	74
Resource Maintenance	75
Resource Maintenance	76
Item Resource Bill Maintenance	79
Creating the End-Item Load	81
Production Conversion Factor	81
Exercise: Setup	84
Enter and Review a Forecast	84
Create a Labor Resource	85
Add a Family Item	85
Create an Item Resource Bill	86

Chapter 4 Using Master Scheduling and RCCP87

Course Overview	88
Using Master Scheduling and RCCP	89
Processing Demand and Supply	90
Master Schedule Order Maintenance	92
Master Schedule Order Maintenance	93
MPS using Forecast Maintenance	95
Master Schedule Summary Inquiry	96
Master Schedule Detail Inquiry	98
Master Schedule Order Browse/Report	99
Master Schedule Order Browse	100
Master Schedule Order Report	101
Sales Order Maintenance - Abnormal Demand	102
Sales Order Maintenance - Abnormal Demand	103
Forecast Worksheet Maintenance	104
Seasonal Build Maintenance	105
Seasonal Build Browse/Report	107
Seasonal Build Browse	108
Seasonal Build Report	109
Master Schedule Summary Inquiry/Report	110
Master Schedule Summary Inquiry	111
Order Promising	113
Available-to-Promise (ATP)	113
Calculation	114
Cumulative Available-to-Promise (ATP)	114
Master Schedule Summary Report	115
Master Schedule Summary Report	116
Master Schedule Detail Inquiry/Report	117
Master Schedule Detail Inquiry	118
Master Schedule Detail Report	119
Selective Materials Plan	120
Item Resource Load Summary Inquiry/Report	123
Item Resource Load Summary Report	125
Item Resource Load Detail Inquiry/Report	126
Item Resource Load Detail Inquiry	127
Item Resource Load Detail Report	128
Exercise: Processing	129
Review a Seasonal Build Forecast	129
Rough-Cut Capacity Planning	129
Course Summary	131
Master Schedule Setup	134
RCCP	135
Answers to Master Schedule Setup Study Questions	136

Answers to RCCP Study Questions 137

About This Course

Course Description

QAD designed this course to cover the basics of preparing to implement Master Scheduling and Rough-Cut Capacity Planning (RCCP) in QAD Enterprise Applications. The course includes:

- An introduction to Master Scheduling and RCCP
- An overview of key business considerations
- Setting up Master Scheduling and RCCP
- Using Master Scheduling and RCCP
- Activities and exercises throughout the course
 - Students practice key concepts and processes in Master Scheduling and RCCP

Course Objectives

By the end of this class, students will:

- Analyze some key business issues before setting up Master Scheduling and RCCP
- Set up and use Master Scheduling and RCCP

Audience

- Materials managers and analysts
- Planners, schedulers, and master schedulers
- Implementation consultants, members of implementation teams, and key users

Prerequisites

Recommended training courses:

- *Initial QAD Enterprise Applications Setup*
- Product Structures and Formulas
- Work Orders
- Work Centers, Routings, and WO Subcontracting
- Forecast Simulation
 - General knowledge of the manufacturing industry
 - Working knowledge of QAD Enterprise Applications as it is used in the business

Course Credit and Scheduling

This course is designed to be taught in one day.

Virtual Environment Information

The hands-on exercises in this book should be used with the "Enterprise Edition 2010 - Addons r03 - Training" environment, in the "10USA > 10USACO" workspace.

QAD Web Resources

The QAD Learning and Support pages can be found at

<http://www.qad.com/>

Chapter 1

Introduction to Master Scheduling and RCCP




Course Overview



Course Overview

- ▲ Introduction to Master Scheduling and Rough-Cut Capacity Planning (RCCP)
- ▲ Business Considerations
- ▲ Set up Master Scheduling and RCCP
- ▲ Use Master Scheduling and RCCP

Planning and Scheduling Overview

		
<h3>Planning and Scheduling Overview</h3>		
Activity	Personnel	Planning Horizon (varies with industry)
Strategic Planning	CEO, CFO, VPs, etc.	3-5 years
QAD Enterprise Application Planning and Control Modules		
Product Line Planning	Senior VP's, Plant Managers	Varies
	Forecasting, Master Scheduling, and RCCP	Master Schedulers
		Cumulative Lead Time 
MRP and CRP	Planners, Shop Floor Managers	Cumulative Lead Time

QAD Proprietary MS-INT-050

All plans set expectations about how resources are used and provide reality checks to determine if plans can be implemented. Planning is done by different people at many levels throughout a corporation and QAD Enterprise Applications provides an integrated toolset that is useful at most of these levels.

Note Students unfamiliar with the planning process described by the American Production and Inventory Control Society (APICS) may find it useful to look at planning level integration.

Strategic Planning

Strategic plans set guidelines for production and sales. Because they are done for the longest term, they are the least integrated and least precise of the planning levels. Chief Executive Officers and Chief Financial Officers look beyond the immediate year's demands to set expectations for growth. Strategic plans set out the overall mission, goals, and initiatives for an organization, largely in terms of gross sales or overall income.

Planning Levels Supported by QAD Enterprise Applications

The following planning levels are supported by QAD Enterprise Applications:

Product Line and Resource Planning

Production planning is done in the Product Line Planning module of QAD Enterprise Applications. The check against resources is done in the Resource Planning module.

This tool enables you to:

- Balance sales forecasts, production forecasts, and income forecasts for an entire product line
- Determine whether you have enough resources, in aggregate, to meet the plans

The production plan sets expectations for a:

- Factory
- Site
- Division, or
- Department

Sales forecasts, production forecasts, and income expectations are produced by different people. Various sets of expectations must be balanced to determine the plan's feasibility.

Production plans:

- Define manufacturing output and other activities to satisfy current planned levels of sales
- Incorporate and coordinate all activities
- Provide guidance for producing individual items that make up the product line
- Support the corporate objectives of increasing:
 - Net profit
 - Return on investment (ROI)
 - Cash flow

Product line plans are broken up into end items, planned in the master schedule, and exploded to component plans by MRP.

End-Item Planning

End-item planning is done in the Forecast/Master Plan module of QAD Enterprise Applications. This tool enables you to set production levels in response to actual and forecast demand over a period roughly equivalent to the cumulative lead time.

The cumulative lead time is the longest length of time it takes to produce and ship an item, assuming that nothing is in stock or production.

At this stage, you can develop a rough-cut capacity plan to determine if critical resources will be available. For example, if you want to make 50 items next week but your fabricator only makes 25 in a week, you cannot meet the plan.

The end-item plan sets the number of priority items (end items, level 1 items, service parts, and so forth) that are going to be produced and sets the schedule to produce them.

End-item plans are usually done by master schedulers who:

- Estimate demand for a product
- Determine how many items to produce

Master schedulers modify factory plans to accommodate current situations. The horizon tends to be at least as long as the cumulative lead time.

Component Planning

Component planning is done in the Material Requirements Plan (MRP) module and the plans are checked against capacity in the Capacity Requirements Plan module of QAD Enterprise Applications.

This tool enables you to schedule and issue orders for the items and work that will be needed to support the master schedule. You can use Capacity Requirements Planning (CRP) to determine at a fairly precise level how this plan will load the resources you have at your site.

Component planning enables you to determine which work centers and components will be used to meet the plan. The check is to determine whether the work centers have capacity to meet the schedule.

Items that are not master scheduled will be planned using MRP with the master schedule as input. MRP uses this demand to schedule orders for components.

Planners and shop floor personnel use MRP results to determine manufacturing schedules which have the same time horizon as master schedules.

Enterprise Resource Planning (ERP)

In companies that use Enterprise Resource Planning (ERP), operations planning is the key link between long-term business planning and medium- to short-term planning and execution activities.


ERP calculates target inventory levels that support company objectives for:

- Profitability
- Inventory reduction
- Lead time reduction
- Customer service

ERP also calculates corresponding production demands. These demands eventually pass into:

- Production
- Purchasing
- MRP

Planning and Scheduling Phases

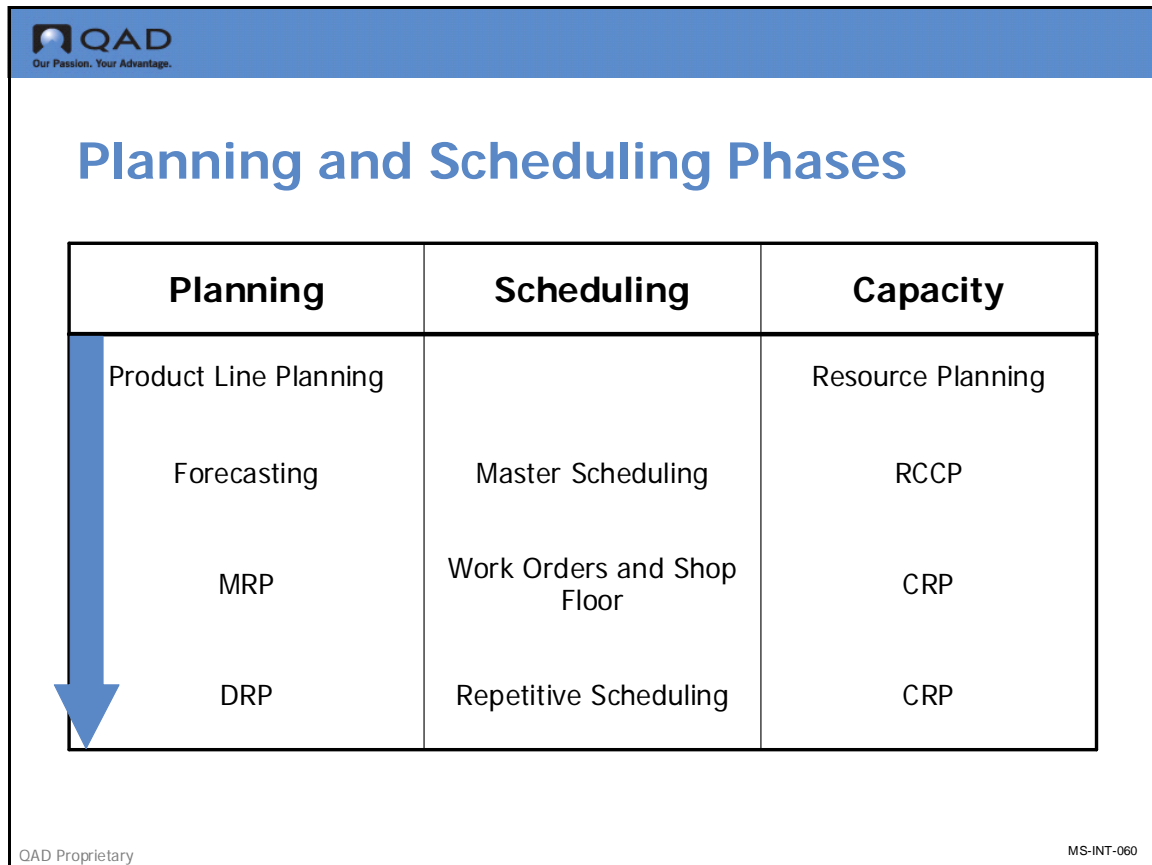

Planning and execution generally move down and to the right through the matrix shown above.

The Product Line

Product line plans generally cover 1 to 3 years, usually shown by months and quarters. They are composed of aggregate forecasts that are converted into end-item forecasts. These detailed forecasts provide input that the master scheduler uses to create a statement of production.

The purpose of a product line plan is to:

- Aggregate forecasts
- Establish aggregate production goals (aligned to corporate goals)
- Plan efficient and cost effective use of production resources, such as machines and manpower
- Outline the level of planned manufacturing output
- Convert demand into a master schedule and rough-cut capacity plan
- Balance sales forecasts, production forecasts, and income forecasts for an entire product line
- Determine whether there are enough resources, in aggregate, to meet the plan

Product line plans are broken into:

- End items planned in the master schedule
- Component plans by MRP

The Forecast

Forecasting and sales orders introduce independent demand into QAD Enterprise Applications.

Independent demand is demand for an item that is unrelated to demand for other items. These demands serve as the primary reason for establishing the master schedule in QAD Enterprise Applications.

- Forecasts
 - Estimate future demand for an item
 - Are typically a sales function
 - Can be an integral part of master scheduling
 - Represent one point of input to the master schedule
- Source of independent demand can be created for any item, but is usually created for:
 - End items
 - Critical subassemblies
 - Service parts

The Master Schedule

Developed by site and item, a master schedule is the key plan that provides primary input to MRP. A master schedule is a statement of production determining:

- Which items to schedule
- When orders are needed
- How much to produce

Master scheduling can be done to:

- Anticipate sales as entered in QAD Enterprise Applications
- Control production when no sales orders are used in inventory replenishment or build-to-stock environments for example

Using master scheduling and MRP is an effective method to:

- Set production levels in response to actual and forecast demand over a period roughly equivalent to the cumulative lead time
- Determine in a rough way (RCCP) whether critical resources will constrain supply

Qualifications and Responsibilities of A Master Scheduler

A master scheduler must have:

- Expertise in manufacturing
- Comprehensive product knowledge
- General business insight
- The ability to:
 - Reduce lead time to bring new products to market
 - Sell ideas and negotiate compromises

- Resolve conflict
- Minimize impact of changing requirements
- Meet customer goals

A master scheduler must know how to prepare data quickly and verify its accuracy in order to deal effectively with:

- Management (overall goals)
- Marketing and sales (available-to-promise)
- Engineering (changing bills of materials)
- Finance (cash flow)
- Distribution (scheduling)
- Customers (demands)
- Vendors (reliability)

The master scheduler is responsible for providing:

- Manpower
- Materials
- Manufacturing capability
- Money (cash flow)
- Management of all logistical activities

Material Requirements Planning (MRP)

MRP is a time-phased priority planning system that calculates material requirements using:

- Product structures
- Inventory status
- The master schedule
- Open order dates

Supply is scheduled and rescheduled to:

- Meet changing demand
- Maintain valid due dates

Capacity Requirements Planning (CRP)

- Determines how much labor and how many machine resources are required for production
 - Calculates workload for a department, work center, or machine
- Used for medium-range capacity management to:
 - Determine and provide the resources required to meet MRP's detailed item schedules

Distribution Requirements Planning (DRP)

- Balances supply and demand for items transferred between sites. It is done by:

- Calculating item requirements
- Creating planned orders
- Managing shipment schedules and transportation

DRP is the extension of distribution requirements, inclusive planning of key resources contained in a distribution system, such as warehouse space, workforce, money, trucks, and freight cars.

Planning and Scheduling Areas of Concern

Activity	Concerns	Expectations vs. Feasibility
Strategic Planning	Sales and Profitability	Income vs. Outlays
Product Line Planning	Factories	Gross Sales vs. Gross Production
Forecasting, Master Scheduling, and RCCP	End Items	Units vs. Resources
MRP and CRP	Work Centers and Components	Planned Production vs. Actual Production

QAD Proprietary

MS-INT-070

Master Schedule

The objective of the master schedule is to:

- Enable implementation of the production plan
- Manage demand and resources
 - Keep priorities in line
 - Plan resources and capacity requirements
 - Ensure good communication between marketing and manufacturing
- Minimize inventory and maximize resource usage

Rough-Cut Capacity Planning (RCCP)

RCCP provides an early warning for schedule problems:

- Provides mid- to long-range capacity planning
- Identifies key material shortages
- Determines labor shortages for critical skills
- Validates the production plan and assists in developing a valid master schedule
- Helps stabilize MRP

- Checks capacity at critical work centers, not at each work center
 - A work center is a specific production area with one or more resources with identical capabilities. It can be considered as one unit for CRP and detailed scheduling

RCCP Compared to CRP


CRP differs from RCCP by taking inventories, orders, lot sizes, and lead time offsets into account. Even though RCCP indicates that sufficient capacity exists to execute the master schedule, CRP may show that capacity is insufficient during specific time periods. CRP:

- Provides the load by work center (detailed capacity)
- Offers detailed work center planning
- Indicates if capacity is sufficient to execute the master schedule
 - Department and work center levels
- Explodes the routings and processes for MRP planned and firm planned orders
 - Updates or creates work order routings
- Determines the start/due dates for each operation using:
 - Work center and shop calendars
 - Back scheduling (start date of the last operation is the due date of the previous operation)

Coordination of planning activities at different levels within a corporation is essential to meeting a company's overall goals. At the plant level, effective coordination of plans will result in:

- Increased throughput
- Decreased inventory
- Reduced operational expense

Statement of Production




Master Schedule

▲ A Statement of Production

Master Scheduled Items

- End Items
- Critical Subassemblies
- Spares/Service Items
- Key Items
- Key Resources

Plan of Action

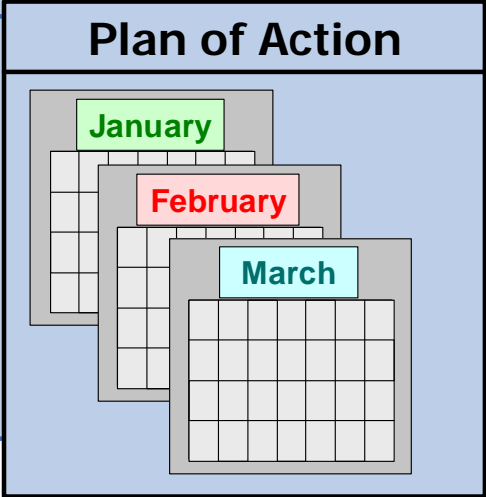

QAD Proprietary
MS-INT-080


A master schedule is a statement of production set by the master scheduler. It is the key plan that drives results on the factory floor. Developed by site and item, it provides primary input to MRP.

A valid master schedule provides the foundation for effective:

- Customer delivery
- Use of plant capacity
- Implementation of the production plan
- Trade-offs between the marketing and manufacturing organizations

Master scheduled items require human judgment to evaluate the implications for capacity, material, cost, and customer service.

Benefits of a Master Schedule

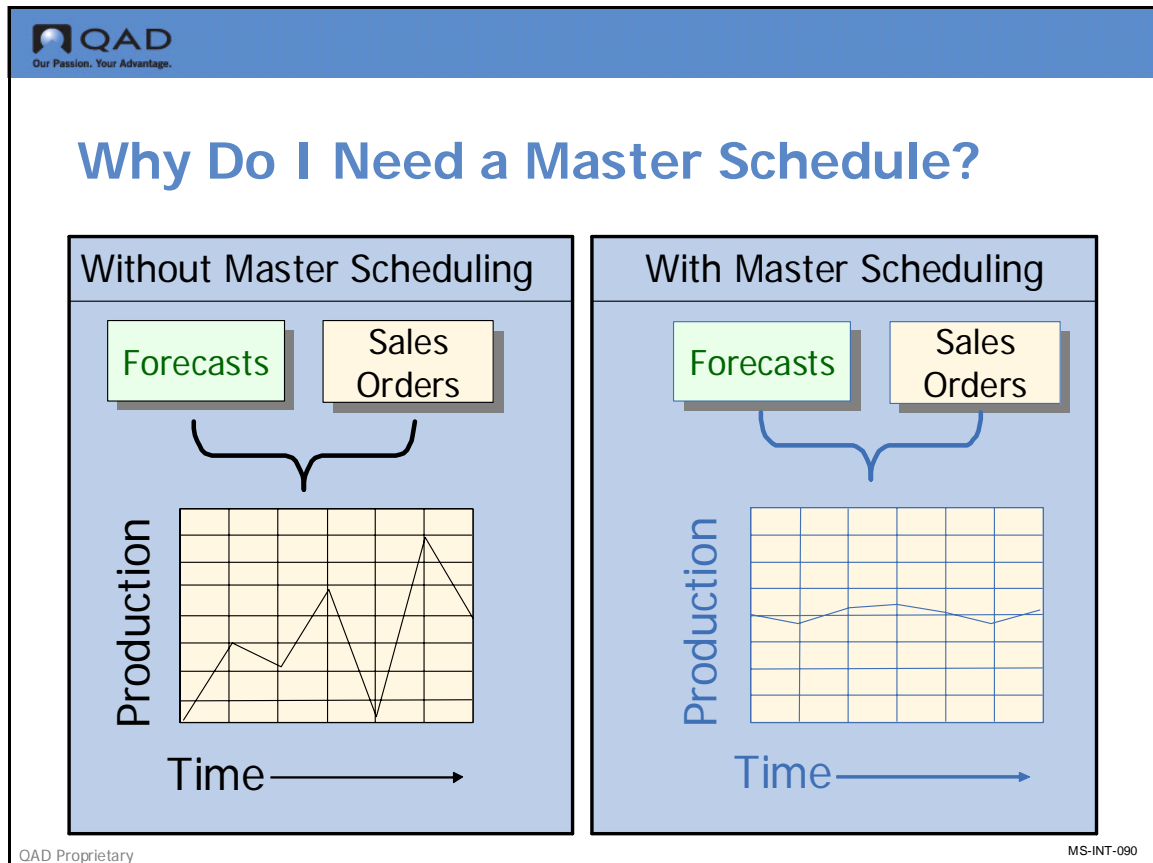

The master schedule acts as a buffer between sales and forecast fluctuations and production. In QAD Enterprise Applications forecasts, along with any confirmed sales orders, are used as input to the master schedule and MRP.

Forecasts and sales orders establish a source of independent demand and are used in calculating the gross requirements for an item. For example, if 100 units per week are forecast, MRP will plan orders to cover this forecast.

As long as actual sales orders due in any period are less than or equal to the forecast in that week, the orders already planned by MRP will cover the requirements.

However, if 100 units have been forecast but there are sales orders for 150 units, MRP needs to plan an extra 50 units.

What MRP will plan in any period is the amount of the sales orders plus any net remaining forecast amount.

Independent Demand

- Demand for an item that is unrelated to demand for other products
 - Finished goods
 - Service parts
 - End items

- Spare parts

Dependent Demand

- Directly related to or derived from the bill of material structure for other items or end products
 - Components
 - Raw materials

Planning Issues

Nervousness

- Fluctuations in MRP would result if forecasts and sales orders were modified or canceled

Overstated Demand


- Total demand would be overstated if:
 - The forecast quantity were added to the sales order quantity

These issues are resolved in QAD Enterprise Applications by:

- Use and application of forecast consumption rules
- Creation of a master schedule which:
 - Anticipates sales
 - Stabilizes production
 - Calculates gross requirements


Note Available-to-promise (ATP) in Master Schedule Summary Inquiry (22.18) gives visibility to customer service.

Terminology



Terminology

- ▲ Available-to-promise (ATP)
- ▲ Available-to-allocate
- ▲ Gross requirements
- ▲ Net requirements
- ▲ Order policies
- ▲ Planning bill of material
- ▲ Seasonal build
- ▲ Time fence



QAD Proprietary
MS-INT-100

Available-to-promise (ATP). ATP is the uncommitted portion of inventory or planned production. It equals the Master Schedule less customer orders due in the period and all subsequent periods before the next Master Schedule scheduled receipt.

Available-to-allocate.

- Based on the calculation specified in the Sales Order Control program
- The quantity on hand less what has already been promised to other orders
 - Sales orders due to ship in the very near future
 - Manufacturing orders which have been released to the shop floor

Note Future requirements or sources of supply are not considered by this calculation.

Gross Requirements. A gross requirement is the total of independent and dependent demand for a component before the netting of on-hand inventory and scheduled receipts.

Net Requirements. In MRP, the net requirements for a part or an assembly are derived as a result of applying gross requirements and allocations against:

- Inventory on hand
- Scheduled receipts
- Safety stock

Net requirements, lot-sized and offset for lead time, become planned orders.

Order Policies. Order policies are sets of procedures for determining the lot size and other parameters related to an order.

Planning Bill of Material. A planning bill of material is an artificial grouping of items or events in bill-of-material format. It is used to facilitate master scheduling and material planning.

Seasonal Build.


An item's inventory build-up prior to expected demand, for example:

- Christmas
- Fall
- Winter
- Spring

Time Fence. A time fence is a policy or guideline established to note where various restrictions or changes in operating procedures take place.

For example, changes to the master schedule can be accomplished easily beyond the cumulative lead time, while changes inside the cumulative lead time become increasingly more difficult (to a point where changes should be resisted). Time fences can be used to define these points.


Rough-Cut Capacity Planning (RCCP)

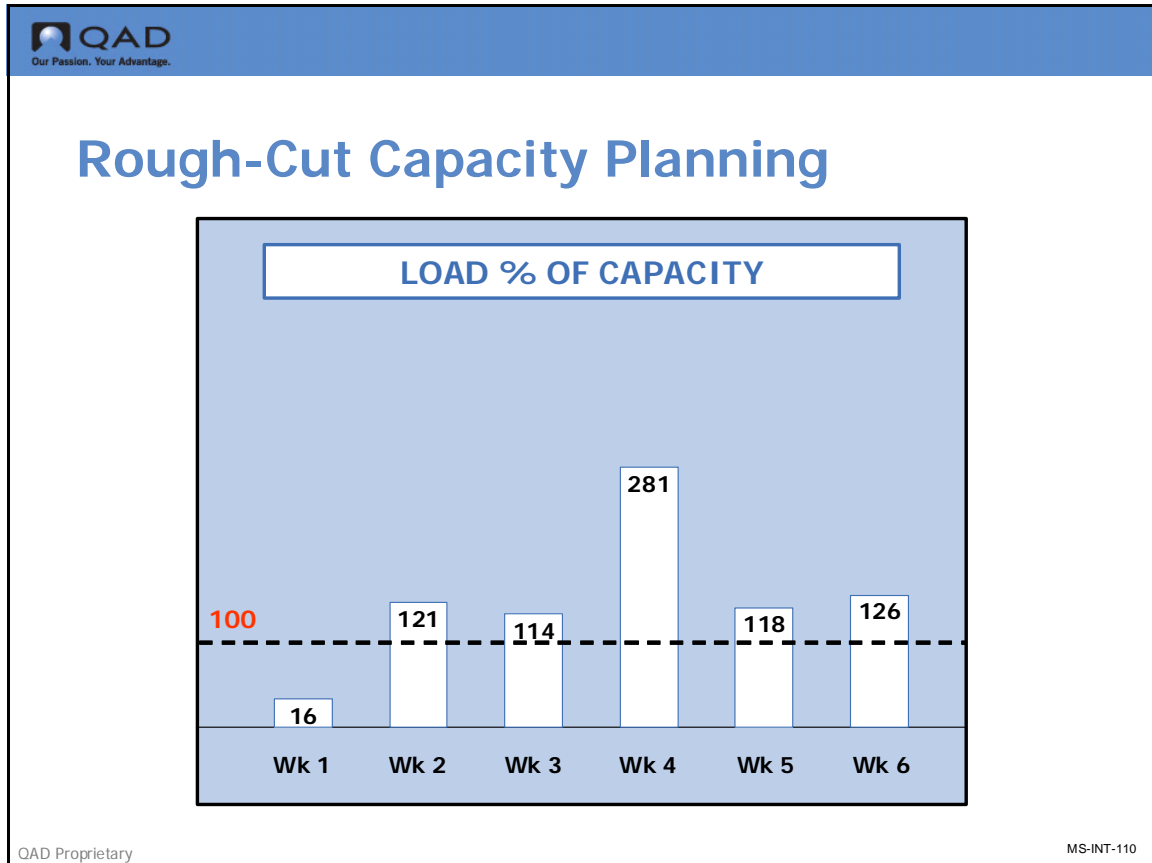

The rough-cut capacity plan provides a tool for:

- Careful evaluation of changes to the master schedule and their impact on material and capacity
- Rough evaluation of potential capacity problems
- Proper balancing of customer needs and manufacturing needs
- Effective stabilization of MRP

Master Schedule and RCCP Uses

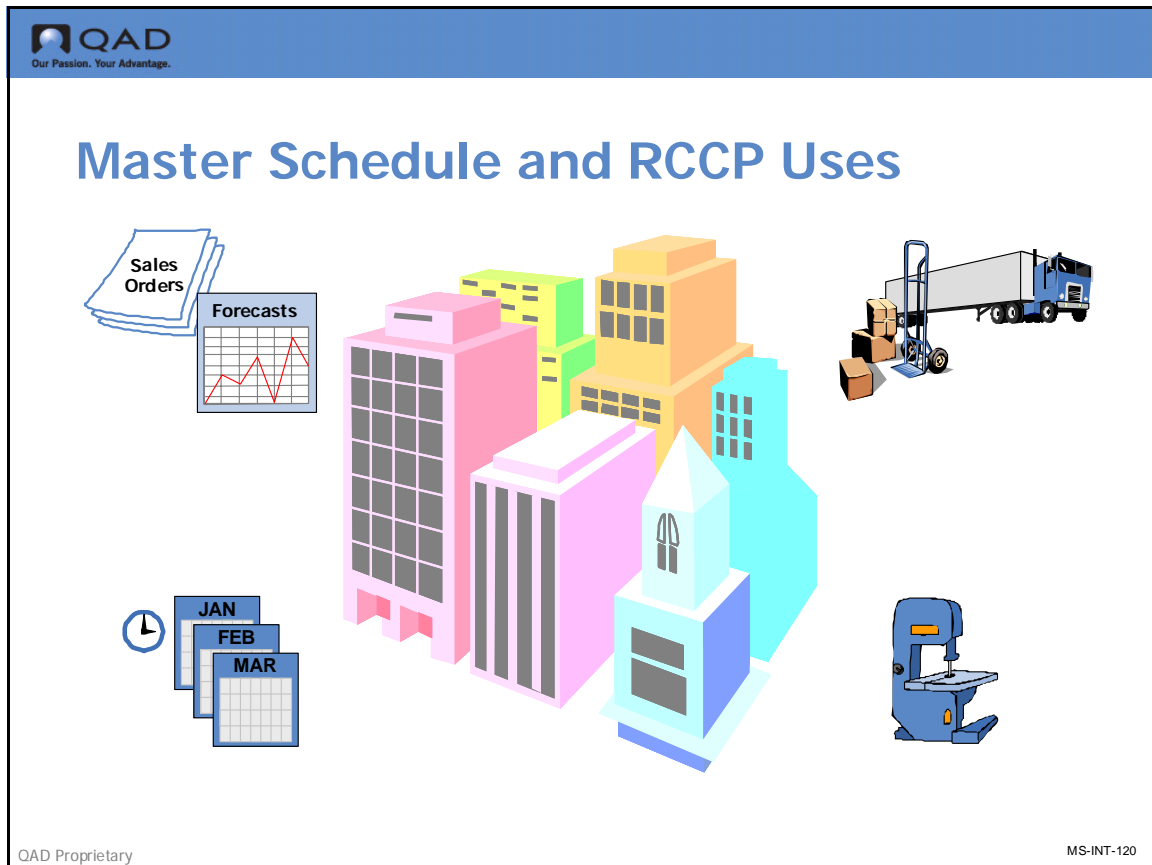

Normal uses of a master schedule include driving RCCP and MRP and planning future production.

- The production plan broken down into buildable units with specific dates for completion
- The production plan will be met if the master schedule is developed to support it

RCCP provides a high-level planning process for key resources which may constrain the execution of the manufacturing plan.

Master scheduling and RCCP should remove most of the capacity constraints before MRP is run.

Course Objectives



Course Objectives

In this course you learn how to:

- ▲ Identify some key business considerations before setting up Master Scheduling and RCCP in QAD Enterprise Applications
- ▲ Set up Master Scheduling and RCCP in QAD Enterprise Applications
- ▲ Use Master Scheduling and RCCP in QAD Enterprise Applications

QAD Proprietary

MS-INT-130

These are the course learning objectives for each chapter in this training guide.

Chapter 2

Business Considerations

Course Overview



Business Considerations

In this course you learn how to:

- ✓ Identify some key business considerations before setting up Master Scheduling and RCCP in QAD Enterprise Applications
- ▲ Set up Master Scheduling and RCCP in QAD Enterprise Applications
- ▲ Use Master Scheduling and RCCP in QAD Enterprise Applications

Business Considerations



Business Considerations

- ▲ Planning
- ▲ Items to Master Schedule
- ▲ Multilevel Master Schedule
- ▲ Production Forecasts
- ▲ Resources That Need RCCP
- ▲ Seasonal Requirements
- ▲ Planning Horizon
- ▲ Time Fence
- ▲ Features and Options
- ▲ Production Constraints


QAD Proprietary

MS-BU-020

There are several business issues to take into consideration before setting up master scheduling and RCCP in QAD Enterprise Applications.

This section does not discuss all of the potential issues, but presents some issues to generate thought and discussion.

Planning Overview

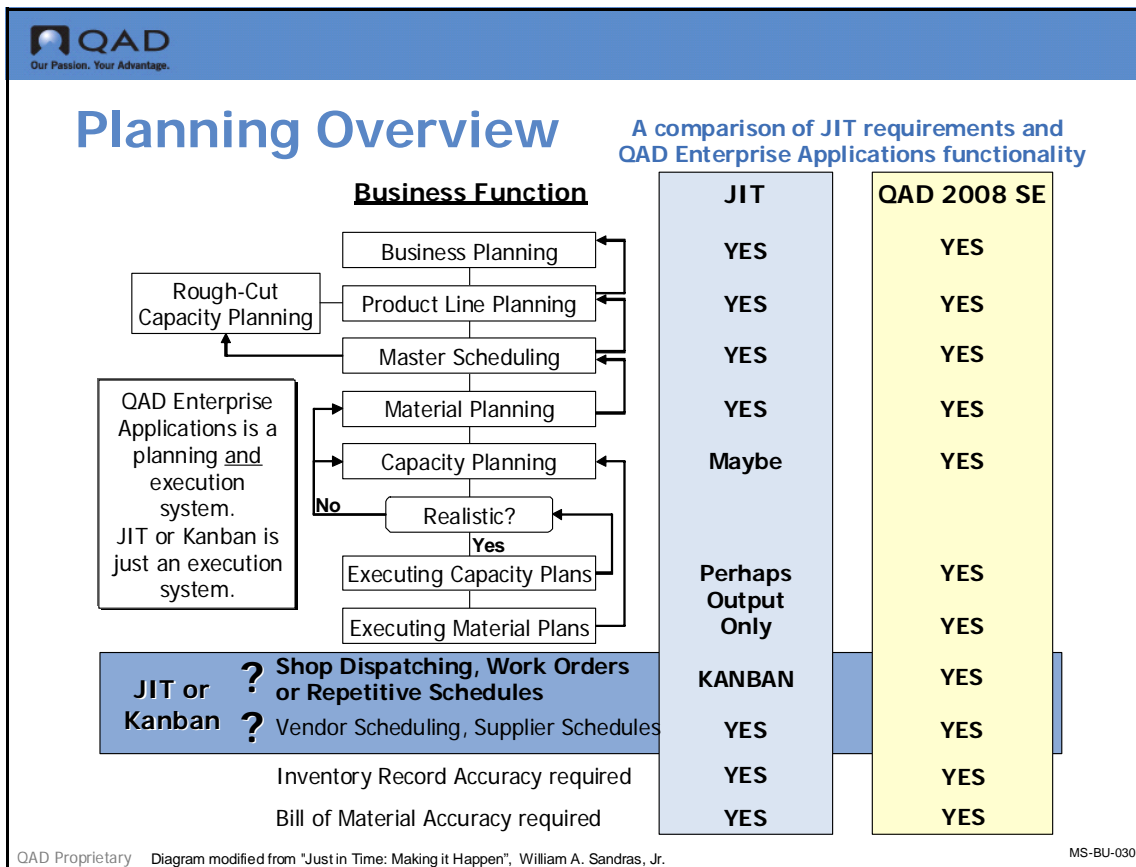

Set planning parameters in:

- Item Planning Maintenance (1.4.7)
- Item-Site Planning Maintenance (1.4.17)

Definition

Planning parameters are established for each item in your database; they govern the way MRP handles the items.

Why Consider?

MRP is only as accurate as the data it processes; your planning parameters should have 98% plus accuracy.

Functionality in QAD Enterprise Applications


The item planning data is the most used information in your database.

Setup Implications

- Inaccurate data can be catastrophic



- A good clean-up of the database is always worthwhile
- Once clean, database update procedures should be in place to maintain data integrity.

Items to Master Schedule



Items to Master Schedule

- ▲ End items
- ▲ Critical subassemblies
- ▲ Spare/service items
- ▲ Key items
- ▲ Key resources

QAD Proprietary MS-BU-040

Definition

Determining which items to master schedule is a reflection of the industry, the products, and the manufacturing processes used in a particular company and requires the expertise of an experienced master scheduler.

Why Consider?

Sometimes, demand for an item is dependent on demand for another item. This is a common occurrence when the master schedules for several sets of items are related through planning bills or product structures.

Functionality in QAD Enterprise Applications

Set Master Schedule to Yes in Item Planning Maintenance (1.4.7) or Item-Site Planning Maintenance (1.4.17) for multiple sites.


- Output for the master schedule is a plan for all items using MRP and product structures
- Input for the master schedule can come from:
 - Forecast Maintenance (22.1) (automatic link)
 - A product line plan

Note In QAD Enterprise Applications, there is no link between the master schedule and the product line plan

Setup Implications


An item can be master scheduled at one site and not another.

Multilevel Master Schedule

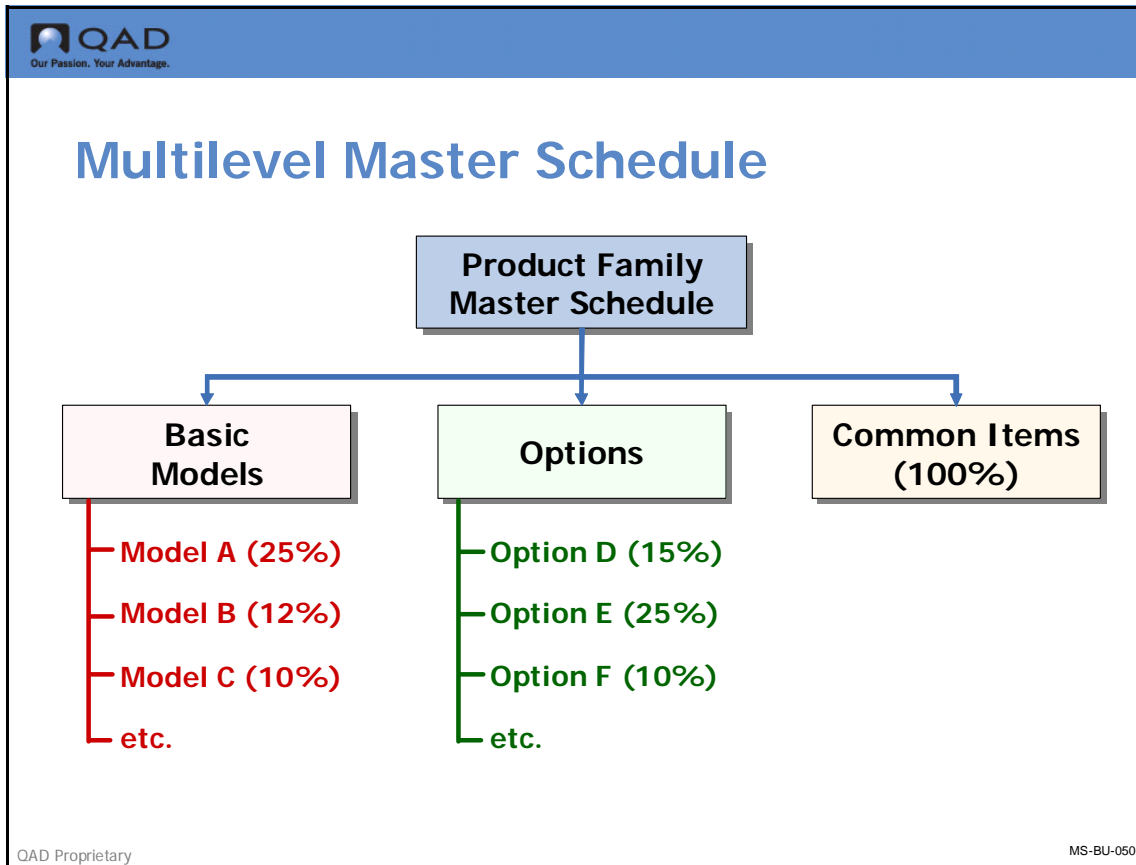

Multilevel master scheduling is an approach where a planning bill of material is used to master schedule an end product or family, along with selected options and accessories.

Production Forecast in QAD Enterprise Applications

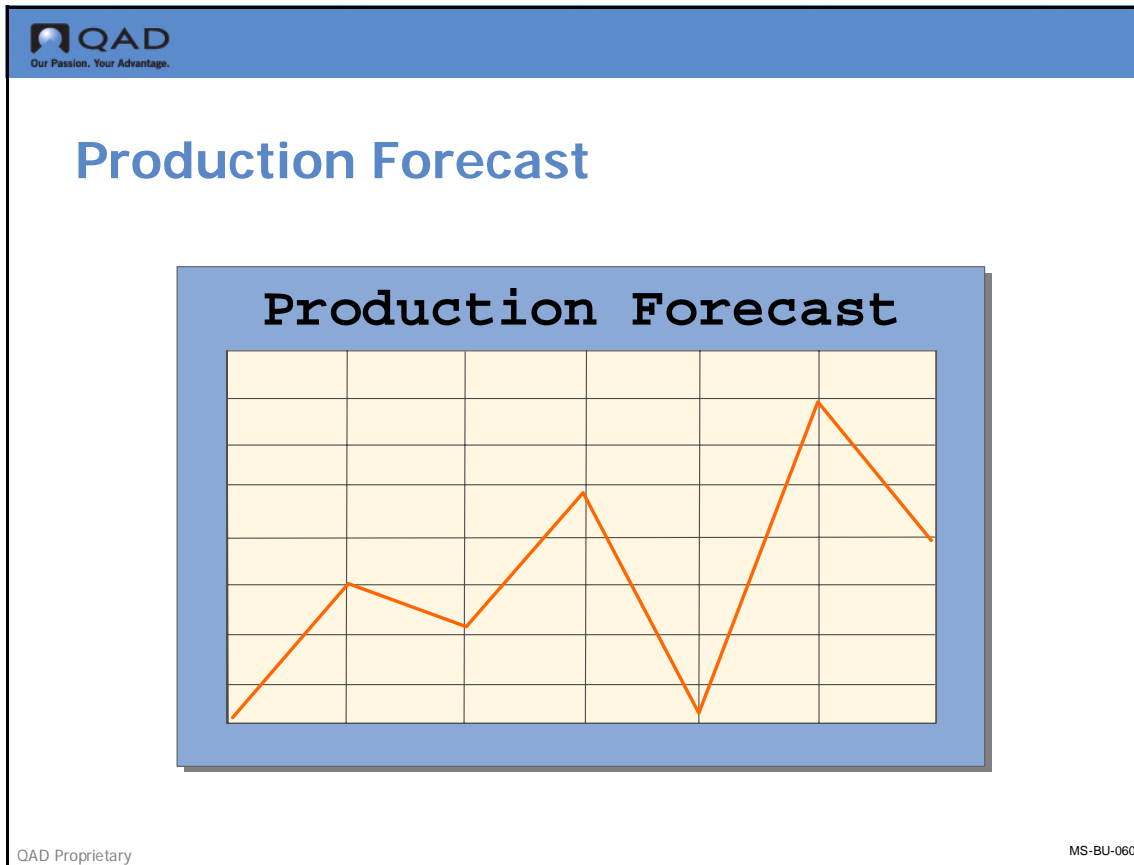

Definition

A production forecast is a system-calculated forecast resulting from a planning bill of material and occurs when using multilevel master scheduling. It estimates the projected level of customer demand for a feature (options, accessories) of a make-to-order or an assemble-to-order product.

When you establish planning bills and forecast and master schedule at the family-item level, the system automatically calculates the derived demand for components of the family or upper-level item. These calculations are based on the available-to-promise quantities for the family-level item and the quantity per and forecast percentage for the components of that family item.

Why Consider?

As forecast for the family-level item is consumed, the available-to-promise quantity for that item changes, resulting in revised calculations for the production forecast the next time MRP is run.

Functionality in QAD Enterprise Applications

- The *production forecast* derives from:
 - The master schedule and forecast percentage specified in the planning bill
- Production forecast amounts:
 - Display in master schedule reports and inquiries


34 Training Guide — Master Scheduling and RCCP

- Contribute to the total demand that MRP regards as input
- Production forecasts are only created for components with structure codes:
 - (P)lanning
 - (O)ption

Setup Implications

- Production forecasts only consume at the higher level

Determine What Resources Need RCCP

 QAD
Our Passion. Your Advantage.

Resources That Need RCCP

Key Resources	Product Groups			
	A	B	C	D
Labor	8.0	6.0	4.1	2.0
Work Center	4.3	7.0	4.8	5.0
Warehouse	6.7	6.7	2.0	2.0
Testing	4.0	1.7	3.8	6.0

QAD Proprietary MS-BU-070

- Develop a resource profile to identify critical resources

Seasonal Build Requirements



Definition

Seasonal demand items require a buildup of an item's inventory prior to its expected demand.

Why Consider?

Although you could enter master schedule orders to adjust to seasonal requirements, identifying a demand as seasonal build prevents MRP from issuing action messages to cancel or delay orders for those items whose demand is not yet apparent.


Functionality in QAD Enterprise Applications

In QAD Enterprise Applications, seasonal build inventory is entered into the system using Seasonal Build Maintenance (22.9).

Setup Implications


Setting inventory to zero enables the items to be promised.

MRP Horizon



MRP Horizon

When Should MRP Be Run?

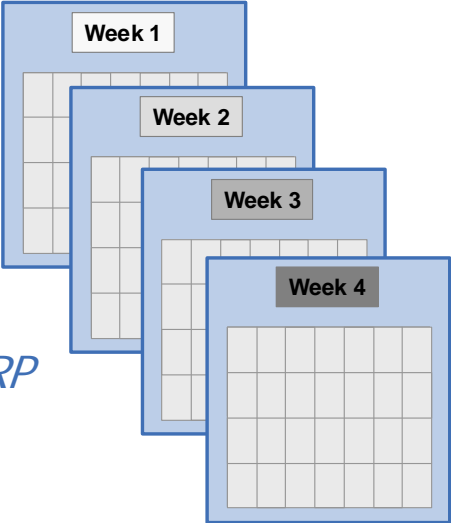

QAD Proprietary MS-BU-090

Definition

- Amount of time the master schedule extends into the future

Why Consider?

MRP only processes material requirements within this horizon and ignores activity outside this horizon.

- Need to allow time for:
 - Ordering components
 - Capacity changes of primary work centers or key suppliers
 - Minimum cumulative lead time

Functionality in QAD Enterprise Applications


- Set the planning horizon in the MRP Control program
- Ensure that all items are replanned by running the Regenerate Materials Plan (23.2)

Since MRP ignores activity outside of the planning horizon, make the horizon at least one day longer than the longest cumulative lead time (30 days is recommended as a minimum). Use the Cumulative Lead Time Report (13.12.16) or the Lead Time Picture Report (13.12.17) to find the longest cumulative lead time in your database.

Setup Implications

- If the horizon is changed, items are not automatically flagged for net change replanning, run Regenerate Materials Plan (23.2)

Time Fence

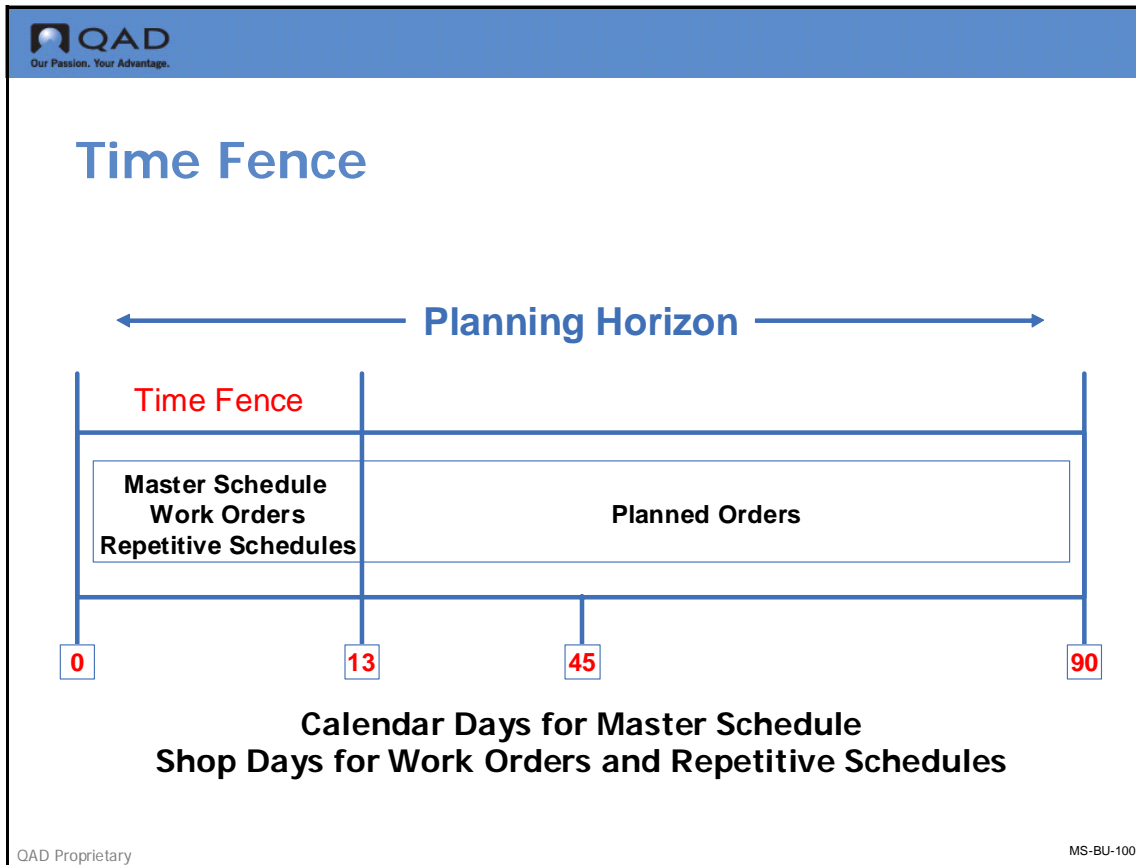

Definition

The number of calendar days inside of which MRP should not automatically make changes. To manually control the schedule for a period of time set the time fence to mn days and MRP:

- Adds the number of days time fence to the system date
- Does not create any planned orders within this time period

Note Time fence is most often used with master scheduled items.

Why Consider?

The time fence gives the master scheduler manual control within the time fence period. MRP is allowed to create planned orders automatically outside of the time fence.


Functionality in QAD Enterprise Applications

The value entered in Item Master Maintenance (1.4.1) is used as the default for all sites. It may be changed manually for any site as needed.

Setup Implications

The time fence designates a period of calendar days from the system date inside of which MRP will not create or change existing planned orders. Order action messages, however, will be generated if necessary. MRP will provide action messages over the near-term horizon.

Features and Options

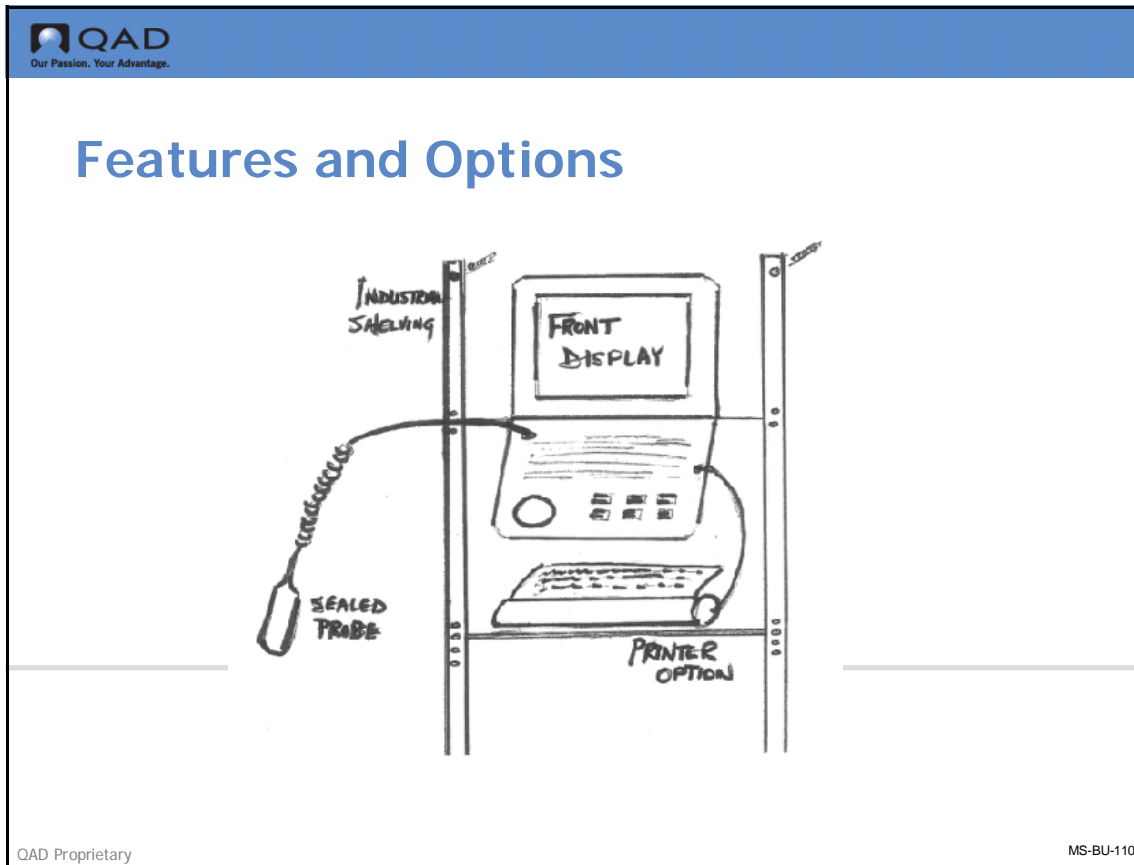

Definition

Components of the family item in the planning bill can be either the actual manufactured items or configured products, or item groups representing common components or selected features and options.

Why Consider?

Directly forecast the family/models and forecast options by percent of family.


Functionality in QAD Enterprise Applications

The top-level item of a multilevel master schedule product structure represents the family of buildable products that can be configured from a set of available models and options.

Setup Implications

For master scheduling purposes, it is not possible to forecast accurately the detailed combinations of potential products that can be manufactured and sold. Forecasting at the family-item level or the option-item level is accurate and can drive the master scheduling process.

Production Constraints



Production Constraints

- ▲ Machine capacity
- ▲ Work center capacity
- ▲ Labor capacity
- ▲ Material
- ▲ Policies and procedures

QAD Proprietary MS-BU-120

Definition

A production constraint is any element or factor that prevents a system from achieving a higher level of performance with respect to its goal.

A priority item plan will help resolve production issues. It sets the number of priority items (end items, level 1 items, service parts, etc.) that are going to be produced and plans the schedule to produce them. The check on this plan is the availability of critical resources.

If you want to make 150 items next week, but your machine only makes 125 in a week, you cannot meet the plan. A component plan determines which work centers and components will be used to meet the plan. The check is to determine whether the work centers have the capacity to meet the schedule.

Why Consider?

A master scheduler must consider and remove potential production constraints when preparing the master schedule and rough-cut capacity plan. A constraint could be physical (machine capacity or lack of material) or managerial (policies and procedures).

Functionality in QAD Enterprise Applications

The master scheduler makes the best use item-level RCCP by considering constraints. RCCP is implemented in QAD Enterprise Applications using Item Resource Load Summary Inquiry.

Setup Implications

The master scheduler tests scheduled production quantities against available resources. This rough-cut capacity plan tests end-item production.

Summary



Review

- ▲ Processes and Procedures
- ▲ Reporting Requirements
- ▲ Customer Expectations
- ▲ Product Configuration

Chapter 3

Set Up Master Scheduling and RCCP

Course Overview



Set up Master Scheduling and RCCP

- ✓ Identify some key business considerations before setting up Master Scheduling and RCCP in QAD Enterprise Applications
- ✓ **Set up Master Scheduling and RCCP in QAD Enterprise Applications**
 - ▲ Use Master Scheduling and RCCP in QAD Enterprise Applications

Simulated Forecasting




Master Schedule and RCCP Setup



- ▲ Simulated Forecasting
- ▲ Item and Item-Site Planning Maintenance
- ▲ MRP Control
- ▲ Holiday/Calendar Maintenance
- ▲ Resource Maintenance
- ▲ Item Resource Bill Maintenance

Balance Demand and Supply

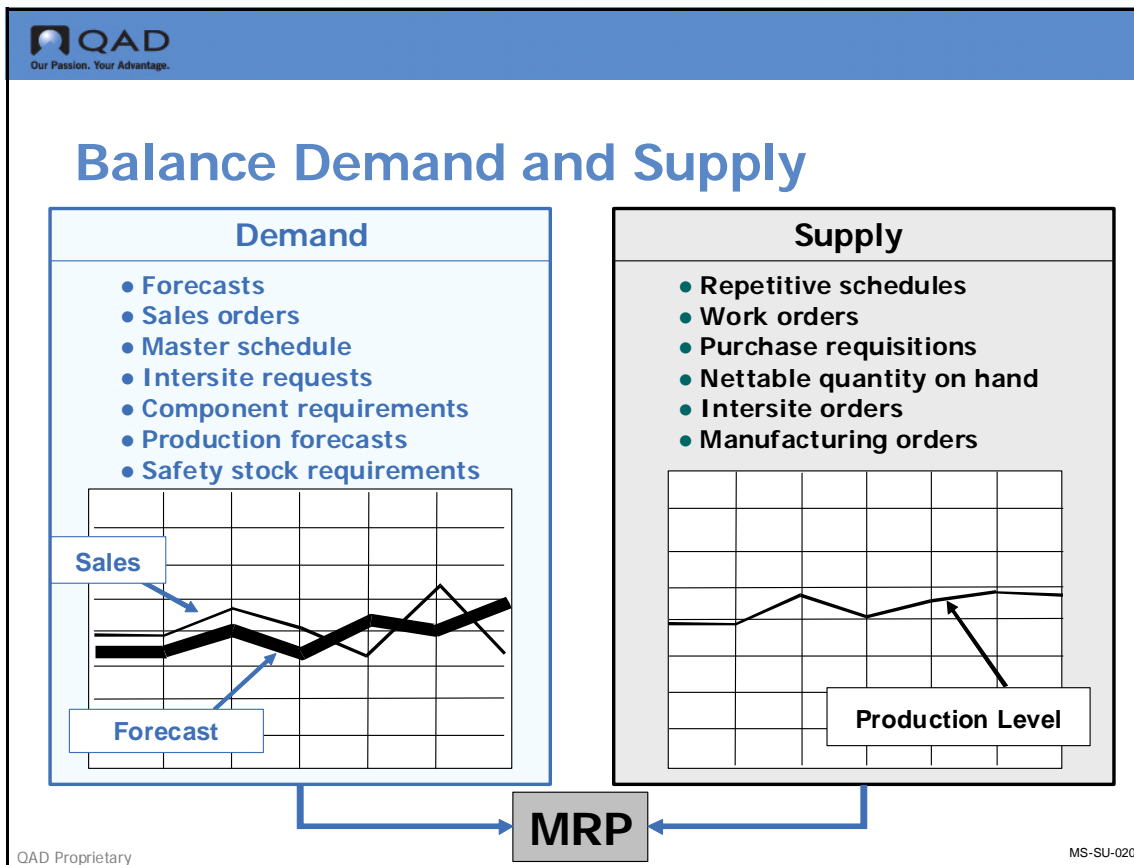

The master schedule represents supply which then creates component demand for MRP. Master scheduled items require human judgment to evaluate the schedule and its effects on capacity, material, cost, and customer service. The master scheduler creates required supply orders to meet demand after considering requirements for:

- Independent demand (forecasts and sales orders)
- Dependent demand (related to or derived from the BOM structure for other items or end products), especially when scheduling for important spare parts
- Abnormality
- Seasonality
- Consumption

Sales order demand is the quantity of an item sold, as recorded on confirmed sales orders or required ship schedules. The system recognizes item quantities ordered as demand when a sales order has been confirmed.

- Confirmed = Yes in Sales Order Maintenance (7.1.1)
- A customer planning or shipping schedule has been changed to a required ship schedule using Required Ship Schedule Update (7.5.5)
- Selective Required Ship Schedule Update (7.5.6)

Sales order demand:

- Consumes shipment forecasts based on the item number, site, quantity, and due date recorded on the sales order or customer schedule
- Is abnormal if the quantity or source of demand is not characteristic of quantities anticipated by the current forecast and should not be used to plan future forecasts

Item and Item-Site Planning Maintenance



Master Schedule and RCCP Setup



- ▲ Simulated Forecasting
- ▲ Item and Item-Site Planning Maintenance
- ▲ MRP Control
- ▲ Holiday/Calendar Maintenance
- ▲ Resource Maintenance
- ▲ Item Resource Bill Maintenance

Identify Master Scheduled Items

The screenshot shows the 'Item-Site Planning Maintenance' window for Item Number: 01010 at Site: 10-100. The 'Mstr Sched' checkbox is checked, indicating the item is master scheduled. Other fields include Order Policy (POQ), Order Qty (0), and various lead times.

Item Number: 01010
Unit of Measure: EA

Item Number: 01010
Site: 10-100
UM: EA

Description: Medical Ultrasound

Item Planning Data

Mstr Sched: Mstr Sched:

Plan Orders: Plan Orders:

Time Fence: 0 Time Fence: 0

MRP Required: MRP Required:

Order Policy: POQ Order Policy: POQ

Order Qty: Order Qty: 0

Batch Qty: Batch Qty: 0

Order Period: 7 Order Period: 7

Safety Stock: Safety Stock: 0

Safety Time: 0 Safety Time: 0

Reorder Point: Reorder Point: 0

Item Rev: D Item Rev: D

Issue Policy: Issue Policy:

Buyer/Planner: 1-01 Buyer/Planner: 1-01

Supplier: Supplier:

PD Site: 10-100 PD Site: 10-100

Purchase/Manufacture: M Purchase/Manufacture: M

Configuration Type: Configuration Type:

Insp Location: 030 Insp Location: 030

1.0 Insp Req: 1.0 Insp Req:

Inspect LT: 0 Cum LT: 0 Inspect LT: 0 Cum LT: 0

Mfg LT: 4 Pur LT: 0 Mfg LT: 4 Pur LT: 0

ATP Enforcement: NONE ATP Enforcement: NONE

Family ATP: Family ATP:

ATP Horizon: 0 ATP Horizon: 0

Run Seq 1: Run Seq 1:

Run Seq 2: Run Seq 2:

Phantom: Phantom:

Minimum Order: 1 Minimum Order: 1

Maximum Order: 5 Maximum Order: 5

Order Multiple: 1 Order Multiple: 1

Op Based Yield: Op Based Yield:

Yield Percent: 100.00% Yield Percent: 100.00%

Run Time: 17.000 Run Time: 17.000

Setup Time: 7.500 Setup Time: 7.500

EMT Type: NON-EMT EMT Type: NON-EMT

Auto EMT Processing: Auto EMT Processing:

Network Code: Network Code:

Routing Code: U-001 Routing Code: U-001

BOM/Formula: BOM/Formula:

QAD Proprietary Item-Site Planning Maintenance (1.4.17 MS-SU-040

To define an item as master scheduled, set Master Schedule = Yes for that item in:

- Item Master Maintenance (1.4.1)
- Item Planning Maintenance (1.4.7) or
- Item-Site Planning Maintenance (1.4.17) (for multisite environments)
 - Most items are set up with Plan Order = Yes
 - Sometimes master schedule items have this flag set to No

If criteria at each site are the same, use Item-Site Planning Maintenance (1.4.17) (the default for all sites). The system looks at item master data only when no site-specific data has been entered, or when dealing with the item at the default site established in Item Master Maintenance (1.4.1).

Note Master schedules can be created and maintained entirely by master schedulers entering firm planned orders using Master Schedule Order Maintenance or Work Order Maintenance.

Item Planning Maintenance

Item Planning Maintenance (1.4.7)

QAD Proprietary

MS-SU-050

Master Sched. This flag = Yes for master scheduled items. These items may be planned separately using Selective Materials Plan (23.3). This allows development of the master schedule for:

- Independent demand items
- Planning for dependent demand items

Plan Orders. Most items are set up with Plan Order = Yes.

Sometimes master scheduled items have this flag set to No, allowing manual interaction with the system.

Indicates whether Material Requirements Planning (MRP) should create planned orders for this item. Planned orders are orders with a suggested order quantity and due date calculated by MRP to meet planned future demand.

The Plan Orders flag operates in combination with the Order Policy. If Order Policy is blank, MRP does not plan this item, regardless of the Plan Orders flag. No requirements or action messages are generated.

Time Fence. Time fence is most often used with master scheduled items. It is the number of calendar days inside of which MRP should not automatically make changes to the plan.

- MRP adds the number of days time fence to the system date and does not create any planned orders within this time period

- MRP will delete any planned order (either inside or outside of the time fence) if there is no demand generated for the item
- On firm orders, if change is needed, MRP creates an action message alerting you to what must be done
 - The message “Time Fence Conflict” reminds you why MRP didn't make the change
- To control the schedule manually for a period of time (the next two weeks, for example), set the time fence to 14 days

MRP Required. A system maintained flag indicating whether an item needs to be replanned

- Net Change Materials Plan (23.1) determines which items to include using this flag
 - Does not replan all items; only items flagged MRP Required = Yes
- An item is automatically flagged for replanning whenever a change is made that affects order timing or quantity, such as:
 - Planning data
 - Inventory balance
 - Product structure
 - Purchase requisitions and orders
 - Sales orders
 - Work orders
 - Master schedule
 - Repetitive schedule
 - Forecast
- If MRP Required = Yes, it reflects changes made after the item was planned by MRP

Order Policy. A code controlling the MRP process for this item/product. Values may be:

- Period Order Quantity (POQ)
 - A planned order is created to cover the requirements for a specified number of calendar days, as specified in Order Period.
- Fixed Order Quantity (FOQ)
 - Planned orders are created with the order quantity specified in the Order Qty field
 - If the value for Min Ord is greater than Order Qty, planned orders are created with the order quantity specified in the Min Ord field instead
 - Order Qty must be greater than zero (even if Min Ord is greater than zero) for creating planned orders
- Lot for Lot (LFL)
 - A separate MRP planned order is created to satisfy each net requirement
 - If there are many sources of demand, MRP creates many planned orders
- One Time Only (OTO)
 - A single order is created with an order quantity of one
 - Could be used to plan project activities and milestone events that happen only once
- Blank

- Obsolete parts, reorder parts, Kanban
- MRP will not calculate

Note Any other non-blank value is processed as LFL.

Whenever a net requirement exists, MRP creates a planned order to fill it. The quantity and due date of the order are determined by the order policy, lead time, and order modifiers.

- If the Order Policy is not blank and the Plan Orders flag = Yes, MRP plans the item
- If the Order Policy is not blank and the Plan Orders flag = No, then MRP plans the item but does not create planned orders
 - Only action messages are created, suggesting what orders should be entered manually
- If Order Policy is blank, MRP does not plan this item, regardless of the Plan Orders flag
 - No requirements or action messages are generated

The traditional technique for managing the master schedule is to enter and maintain master schedule orders manually, using action message reports.

This process becomes unwieldy if you have a large number of master scheduled items, but may work quite well in some situations. To do this, master scheduled items should be set up with the following:

- Master Schedule = Yes
- Plan Orders = No
- Order Policy = any value but blank

Order Qty. The normal order quantity for this item or base process

- If this item has an Order Policy of FOQ, all MRP planned orders are created with this quantity
- For manufactured items, order quantity has another use
 - Identifying the normal or average order quantity of the item
- When manufacturing costs are calculated using Routing Cost Roll-Up
 - Setup costs are divided by this order quantity
- When manufacturing lead times are calculated, they are stated in terms of this order quantity
- If this quantity = zero, the system assumes an order quantity of 1 for cost calculations only
- Not used for co-product or by-product items when planned from a base process
- In a process environment, item Order Quantity should always be the same as the formula Batch Quantity
 - Must be done manually

Warning This value affects both cost and lead time calculations and can significantly impact scheduled due dates. Order due dates are determined using the standard manufacturing lead time (for the standard order quantity). If orders are entered for a much different quantity, due dates must be adjusted manually.

Batch Qty.

- A system maintained field recording the normal batch quantity for an item
 - Used only with formula/process functions

- Ingredient quantity per and process operation run times are stated in terms of batch quantity
- This quantity is updated by the Batch Quantity Change function

Whenever you change the formula Batch Quantity, make sure that you also change the item Order Quantity. These should always be the same. This must be done manually.

Order Period. This field operates only if the Order Policy is set to POQ. Then MRP looks ahead this number of days when calculating net requirements. One planned order is created to cover the requirement for this period.

- Validated against predefined values, if any, entered in Generalized Codes Maintenance (36.2.13)
- Number of calendar days to cover by one MRP planned order (default is 7)

Safety Stk. Safety stock is the quantity of this item to be maintained in inventory as protection against fluctuation in demand and/or supply. Safety stocks may be particularly important for critical items, a shortage of which can shut down production.

- MRP processing considers safety stock a requirement and schedules planned orders to cover it
- As soon as quantity on hand falls below the safety stock quantity, MRP plans an order
- Safety stock and safety time can inflate inventory levels
 - Safety stock can trigger MRP planning an order even if there is no “real” demand
 - Safety time consistently plans to have inventory on hand before it is actually needed

Note Reorder Report (3.6.2) is the only report in the system that shows safety stock.

Safety Time.

- MRP schedules planned orders to be received this many days early
- A hedge against late deliveries

Reorder Point. The inventory level at which this item should be reordered

PO Site. The PO site entered on the requisition determines which purchasing department takes action on this requisition.

Pur/Mfg.

- Purchase/manufacture code controls how the system:
 - Explodes forecasts
 - Plans and creates orders
 - Calculates costs for the item
- Code options include:
 - Purchased (P), DRP (D), manufactured (M), routable (R), configured (C), line manufactured (L), flow scheduled (W), and family (F)

Configuration. Allows users to determine if a configured item is assemble-to-order (ATO) or a kit (KIT).

- ATO
 - A discrete end item in itself, produced from a combination of various components

- The configuration defines components or ingredients of a finished product
- KIT
 - A set of items that are picked for shipment
 - No real assembly takes place
 - Not a physical entity in and of itself; it only exists as a logical superset of its components

Mfg LT. The normal or average number of working days it takes to manufacture this item

Pur LT. Normal number of calendar days it takes to complete a purchasing cycle for this item

Inspect. Indicates whether this item is to be inspected after receipt

Ins LT. The normal or average number of working days needed to inspect this item after it is received

Cum LT. The longest possible length of time it would take to have this item/product available if you started today with no components in stock

- QAD Enterprise Applications looks at the manufacturing lead time of this item and its subassemblies, and the purchasing lead time of the raw materials to determine the critical path

Example You are making washing machines from all purchased components. Most components have a purchasing lead time of 4 days or less, except motors which have a purchasing lead time of 20 days. If it takes 2 days to assemble the machine, the cumulative lead time for a washing machine is 22 days, the longest possible time.

Network.

- A code used to identify a set of sourcing relationships
 - Only works if Pur/Mfg Code = D (DRP)

Routing Code.

- A code identifying the routing or process normally used in the manufacture of this item
- Operates only for manufactured items
- Accesses the routing operation steps to:
 - Calculate product cost
 - Plan for material and capacity

BOM/Formula.

- A code identifying the product structure, formula, and/or co-product/by-product structure normally used to manufacture this item
 - For co-products/by-products, this is the base process code

Issue Policy. A code indicating whether this item should be issued on work order picklists

Phantom. Indicates if this item is normally stocked or is put together as part of a higher level assembly

Min Ord. The minimum quantity of this item to be ordered on a single order

- MRP uses Min Ord to determine the quantity of planned orders, regardless of the Order Policy
 - If net requirement is below this amount, MRP creates an order for this minimum quantity
 - If an existing order is below this minimum, MRP creates an action message

Max Ord. Zero (default) means there is no maximum of this item to be ordered on a single order.

- If MRP calculates a requirement greater than this, it creates a planned order for the amount needed
- However, any time MRP sees an order for more than this quantity, it creates an action message

Ord Mult. The multiple in which orders for this item are placed

- Used only when Order Policy = POQ or LFL
 - Then MRP uses it to determine the quantity of planned orders
 - The net requirement is rounded up to a multiple of this number

Example If the order multiple is 50 and the net requirement is 432, MRP creates a planned order for 450.

Yield%. The percentage of any order expected to be in usable condition

- Applies to both purchased and manufactured items
- If the yield is less than 100%, then MRP plans orders for more than needed

Example If the net requirement is 100 and the item yield is 50% then the planned order quantity is set to 200.

Run Time. Standard time in decimal hours (excluding setup time) required to make one unit of this item

- The sum of all the operation run times
- This field is for reference only and may appear on some selected reports and inquiries

Setup Time. Standard time required in decimal hours to set up for one lot of this item

- The sum of all the operation setup times divided by the item Order Quantity
- This field is for reference only and may appear on some selected reports and inquiries

EMT Type. This field is used in the Enterprise Material Transfer (EMT) order processing environment.

Auto EMT Processing. This field is used in the multilevel Enterprise Material Transfer (EMT) order processing environment.

Item-Site Planning Maintenance

Item-Site Planning Maintenance

Item:01010 Item Number:01010 (2) Site:10-100

Item Number: 01010 Description: Medical Ultrasound
Site: 10-100 UM: EA

Item Planning Data

Mstr Sched: Buyer/Planner: 1-01 Phantom:
 Plan Orders: Supplier: 10-300 Minimum Order: 1
 Time Fence: 0 PO Site: 10-100 Maximum Order: 5
 MRP Required: Purchase/Manufacture: M Order Multiple: 1
 Order Policy: POQ Configuration Type: Op Based Yield:
 Order Qty: 0 Insp Location: 030 Yield Percent: 100.00%
 Batch Qty: 1.0 Insp Req: Run Time: 17.000
 Order Period: 7 Inspect LT: 0 Cum LT: 0 Setup Time: 7.500
 Safety Stock: 0 Mfg LT: 4 Pur LT: 0 EMT Type: NDN-EMT
 Safety Time: 0 ATP Enforcement: NONE Auto EMT Processing:
 Reorder Point: 0 Family ATP: Network Code:
 Planning Rev: D ATP Horizon: 0 Routing Code: U-001
 Issue Policy: Run Seq 1: BOM/Formula:

Run Seq 2:

Item-Site Planning Maintenance (1.4.17)

QAD Proprietary MS-SU-060

Multisite Environments


Note Takes precedence over Item Planning Maintenance (1.4.7).

Item planning data controls QAD Enterprise Applications planning and manufacturing functions. If an item is used at multiple sites, planning data can be set up differently for each site.

If an item is used at multiple sites, planning data can be set up differently for each site.


- To define an item as master scheduled, set Master Schedule = Yes in Item-Site Planning Maintenance (1.4.17)
- An item can be master scheduled at one site and not at another

Approaches to Master Scheduling



Operational Approaches

- Computer Assisted?
- Fully Automatic?
- Fully Manual?



QAD Proprietary MS-SU-070

There are three approaches to master scheduling in QAD Enterprise Applications:

- 1 Computer assisted (recommended)
- 2 Fully automatic
- 3 Fully manual

Carefully consider these options when setting planning parameters for your items at each site. Each item can be set up in any of these approaches. The next few pages will discuss the options in some detail.

Computer Assisted Approach (Recommended)

Item Planning Maintenance (1.4.7)

To use the computer-assisted approach for master scheduling, set the following values for each master scheduled item:

- Master Schedule = Yes
- Plan Orders = Yes
- Time Fence = cumulative lead time
- Order Policy = any option but blank

Time Fence. Defining time fences for master scheduled items allows MRP to control orders outside of a specified time period and allows the master scheduler to control orders within that time period.

Specify a planning horizon, in calendar days, for each master scheduled item. When MRP plans orders for these items, it will not schedule order due dates within this time fence.

MRP will plan orders to:

- Cover future requirements
- Provide action messages over the near-term horizon
 - In the near term, the master scheduler maintains the master schedule

Note The time fence is where manual control is exerted in computer-assisted planning. The longer the time fence the more manual involvement the master scheduler will have.

Selective Materials Plan

Selective Materials Plan (23.3) allows planning for master scheduled items separately from MRP items. If you use the computer-assisted approach to master scheduling, you may want to:

- Run Selective Materials Plan for master schedule items only
- Adjust the master schedule and rerun Selective Materials Plan as needed
- Run Selective Materials Plan for MRP-scheduled items only

Note Selective MRP plans requirements only for the items selected. At some point you will need to run Net Change MRP to plan lower level requirements.

Fully Automatic Approach

Item Planning Maintenance

Item: 01041 Item Number: 01041 (2) Supplier:

Item Number: 01041 Description: Portable 10mhz
Unit of Measure: EA Ultrasound

Item Planning Data

Mstr Sched: Buyer/Planner: 1-01 Phantom:
Plan Orders: Supplier: Minimum Order: 1
Time Fence: 0 PO Site: 10-100 Maximum Order: 1
MRP Required: Purchase/Manufacture: M Order Multiple: 1
Order Policy: LFL Configuration Type: Op Based Yield:
Order Qty: 0 Inspect: Yield Percent: 100.00%
Batch Qty: 1.0 Ins LT: 0 Cum LT: 0 Run Time: 17.000
Order Period: 0 Mfg LT: 4 Pur LT: 0 Setup Time: 7.500
Safety Stock: 0 ATP Enforcement: NONE Auto EMT Processing:
Safety Time: 0 Family ATP: Network Code: Routing Code: U-001
Reorder Point: 0 ATP Horizon: 0 BOM/Formula:
Item Rev: Run Seq 1: 2:
Issue Policy:

Fully Automatic *Item Planning Maintenance (1.4.7)*

QAD Proprietary MS-SU-090

The master schedule can be generated entirely by MRP. This means that the system has complete control over master scheduled items with no distinction between master scheduled and MRP items. When this approach is used, material plans may change dramatically each time MRP is run. A master schedule order may be expedited one day and canceled the next for example.

To use the fully automatic approach to master scheduled items, set the following values:

- Master Schedule = Yes
- Plan Orders = Yes
- Time Fence= 0
- Order Policy = any option but blank

Fully Manual Approach

Item Planning Maintenance (1.4.7)

QAD Proprietary MS-SU-100

Fully Manual Scheduling


- Master Schedule = Yes
- Plan Orders = No
- Order Policy = Any option other than blank

Enter all master scheduled orders manually. MRP will not generate any planned orders, but will issue action messages suggesting that orders be created if none exist.

Note In a make-to-stock environment it seems unlikely that all master scheduled items would be planned manually. However in a make to order environment it is more likely and in a job shop situation very likely.

There are situations where the master scheduler wants to know the requirement for an item but does not want the system to plan an order that will never be released. One example of this is water used in some food processing. The planner may wish to know how much water this months schedule requires, but will never issue a purchase order to buy the water as it is cover by plant overhead as a utility. The action message will specify the amount of water needed. In contrast some processes used specially processed bottled water that is purchased with a purchase order.

Multilevel Master Scheduling

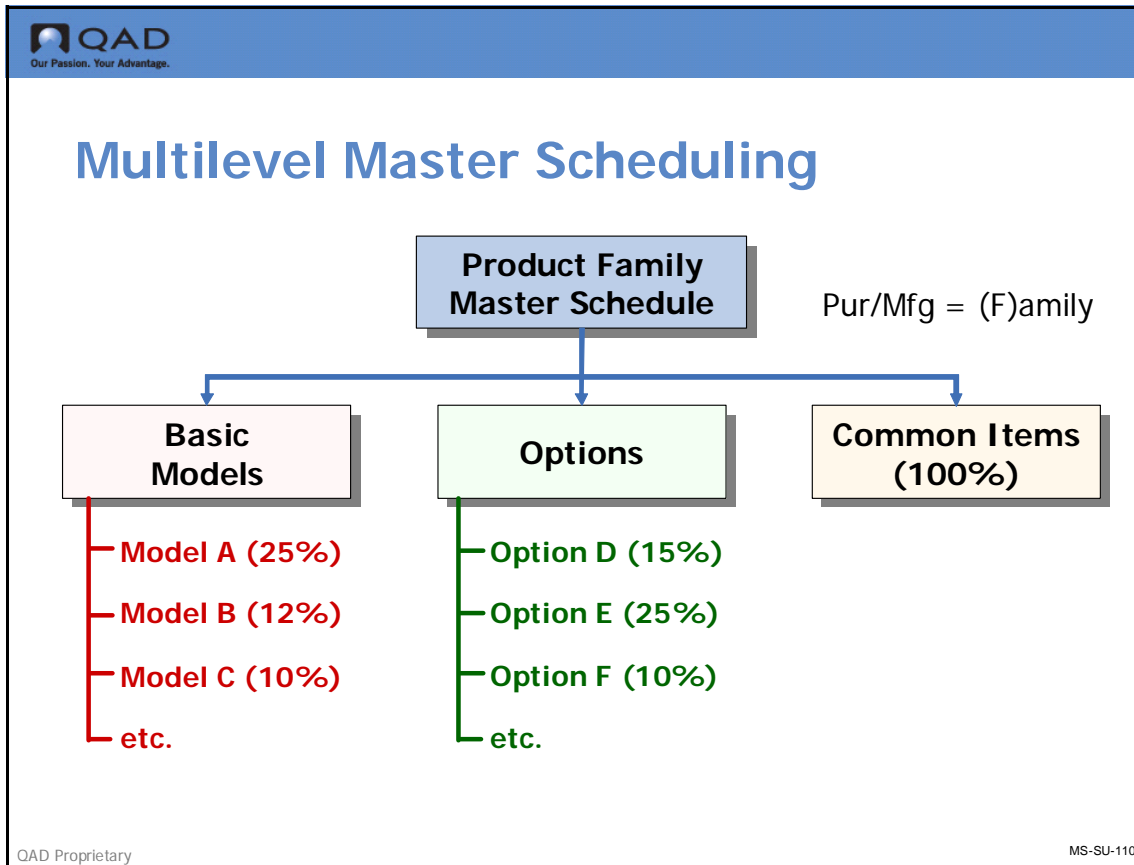

- Plan family-level items using either the fully automatic or computer-assisted technique
- Use MRP to plan orders to generate production forecasts for the components of family items

Sometimes, demand for an item is dependent on demand for another item. This is a common occurrence when the master schedules for several sets of items are related through planning bills or product structures.

- Typical in assemble-to-order environments (automotive, computer manufacturers, etc.)
- Unrealistic to stock all of the possible combinations of end items
- Impossible to accurately forecast all possible combinations of end items for master scheduling

For master scheduling purposes, it is not possible to accurately forecast the detailed combinations of potential products that can be manufactured and sold.

Forecasting at the family-item level or the option-item level is more accurate and can be used to drive the master schedule process.

Typically, the top-level item of a multilevel master scheduled product structure represents the family of buildable products that can be configured from a set of available models and options. It represents an item that is itself never manufactured or stocked.

In QAD Enterprise Applications, such an item is assigned the Pur/Mfg code of [F]amily.

Planning Bills

The screenshot displays two overlapping windows in the QAD software interface. The background window is 'Item Planning Maintenance' for Item 60006 (Monitor Cable). The foreground window is 'Product Structure Maintenance' for the parent item 60004 (Transducer - 10 Mhz). In the foreground window, the 'Purchase/Manufacture' dropdown is set to 'P', the 'Structure Type' is 'P', and the 'Forecast Percent' is 100.00%. Red boxes and arrows highlight these specific settings.

Having identified a family item for multilevel master scheduling, the next step is to identify the component items. In such a product structure the components are the actual:

- Manufactured model
- Manufactured configured product
- Item groups representing common parts or selected options

Using Product Structure Maintenance in QAD Enterprise Applications, items within the family product structure are assigned a:

- Structure code of [P]lanning or [O]ption
- Forecast percentage

The Structure Code settings of P or O dictate how QAD Enterprise Applications will handle the dependent demand forecast driven off of the parent item.

Production Forecasts

As a result of establishing a family planning structure and then forecasting and master scheduling at the family level, QAD Enterprise Applications will calculate the demand for the component items. This derived demand resulting from the family or upper-level independent demand is a Production Forecast.

- The production forecast derives from the:

- Master production schedule, and
- Forecast percentage specified in the planning bill
- Production forecast amounts:
 - Display in master schedule reports and inquiries
 - Contribute to the total demand that MRP regards as input

When planning bills, forecasts and master schedules are established at the family-item level,

QAD Enterprise Applications automatically calculates the derived demand for components of the family or upper-level item.

These calculations are based on the available-to-promise quantities for the family-level item and the quantity per and forecast percentage for the components of that family item.

As forecast for the family-level item is consumed, the available net forecast for that item changes, resulting in revised calculations for the production forecast the next time MRP is run.

Top-Level Items

Usually, the top-level item of a multilevel master scheduled product structure or planning bill represents the entire family of products that can be configured from a set of available models and options.

- Define family items with a Pur/Mfg code of Family (F) in:
 - Item Planning Maintenance (1.4.7) or Item-Site Planning Maintenance (1.4.17)
- Components of the family item in the planning bill can be either:
 - The actual manufactured items or configured products, or
 - Item groups representing common components or selected options

Family-Level Item Values

Set Master Schedule = Yes and Plan Orders = Yes for family-level items.


- MRP calculates net requirements and creates or adjusts planned orders accordingly
- Manually control the schedule for a period of time by setting the time fence appropriately

Time Fence (Optional). MRP adds the time fence to the system date

- MRP does not create any planned orders within that time period
- MRP will delete any planned order if there is no demand generated for the item
- If change is needed on firm orders, MRP creates an action message

Order Policy. Any option other than blank


Example

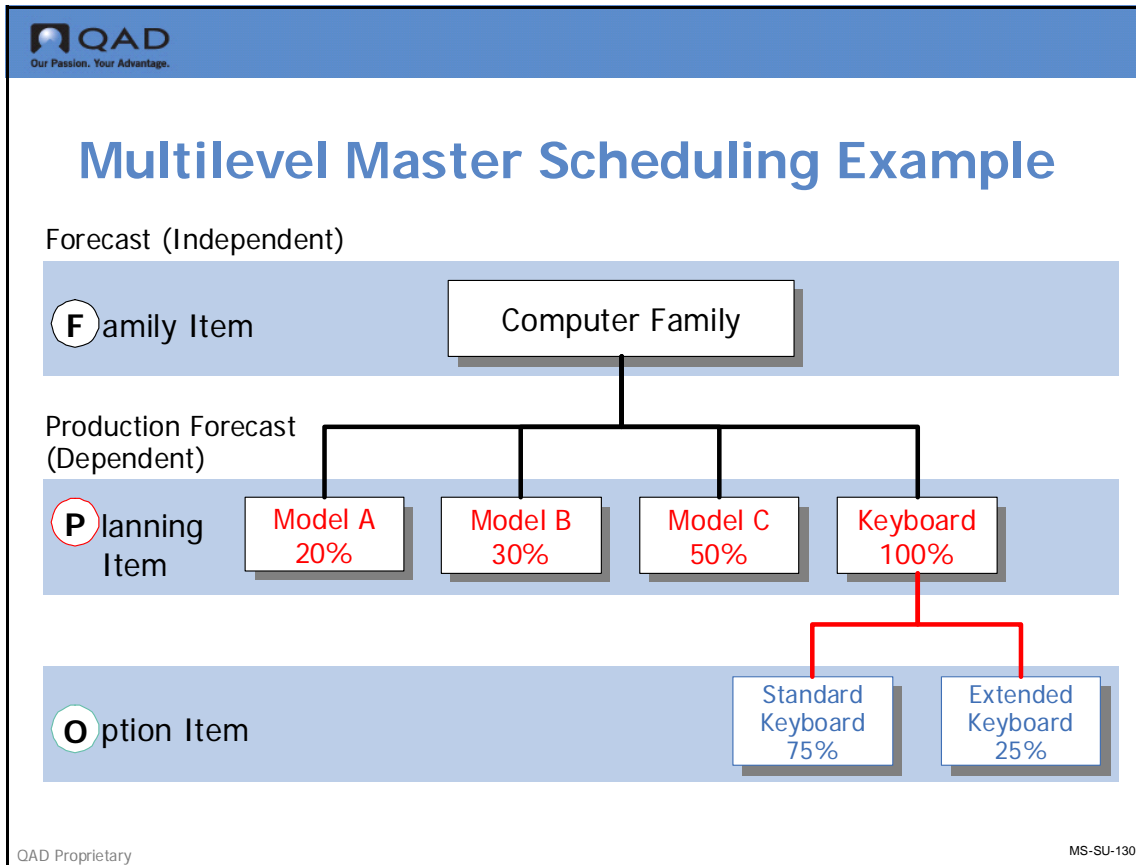


The multilevel schedule consists of forecasts that are exploded by MRP.

Note Discussed in the *Product Structures & Formulas training guide*.

MRP Control



Master Schedule and RCCP Setup



- ▲ Simulated Forecasting
- ▲ Item and Item-Site Planning Maintenance
- ▲ MRP Control
- ▲ Holiday/Calendar Maintenance
- ▲ Resource Maintenance
- ▲ Item Resource Bill Maintenance

QAD Proprietary MS-SU-140

MRP Control – Planning Horizon

The diagram illustrates the relationship between the Time Fence, Longest Cumulative Lead Time, and the Planning Horizon. The Time Fence is set at 7 days, the Longest Cumulative Lead Time is 20 days, and the Planning Horizon is 21 days. The area between the Time Fence and the end of the Planning Horizon is labeled 'Planned Orders'.

QAD Proprietary MS-SU-150

Time Fence.

- Number of calendar days from the system date inside of which MRP will not create or change existing planned orders
 - Order action messages, however, will be generated if necessary
- The time fence is where manual control is exerted in computer-assisted master scheduling

MRP Horizon. The MRP horizon should be at least as long as the master scheduled item with the longest cumulative lead time for the item being scheduled or else key materials may not be planned to be available when required.

- MRP only processes material requirements within this planning horizon

Order Release Horizon. Order Release Horizon is the number of days MRP looks to the future to see when orders are due to be released. In the screen shot the value is seven days. MRP will start creating action messages “order due for release” seven days before the release date.

Warning If the horizon is changed, items are not automatically flagged for net change replanning. Run Regenerate Materials Plan (23.2).

Holiday/Calendar Maintenance



Master Schedule and RCCP Setup



- ▲ Simulated Forecasting
- ▲ Item and Item-Site Planning Maintenance
- ▲ MRP Control
- ▲ **Holiday/Calendar Maintenance**
- ▲ Resource Maintenance
- ▲ Item Resource Bill Maintenance

Calendar Maintenance

Calendar Maintenance

Site: Work Center: Machine:

Work Day	Hours
Sunday: <input type="checkbox"/>	0.00
Monday: <input checked="" type="checkbox"/>	8.00
Tuesday: <input checked="" type="checkbox"/>	8.00
Wednesday: <input checked="" type="checkbox"/>	8.00
Thursday: <input checked="" type="checkbox"/>	8.00
Friday: <input checked="" type="checkbox"/>	8.00
Saturday: <input type="checkbox"/>	0.00

Reference: Generic
Start: 10/25/2010
End: Daily Hours:

Calendar Maintenance (36.2.5)

QAD Proprietary MS-SU-170

Calendar Maintenance (36.2.5) is only relevant for master scheduling when using the fully automatic or computer-assisted method.

- Calendars define:
 - The standard work week for a site and the work centers in it
 - Exceptions to the normal calendar, such as scheduled overtime or shutdown periods
- In a calendar, work days = Yes and nonwork days = No

Note If the Site, Work Center, and Machine are blank, the calendar acts as the default for the entire company (must be blank for RCCP.)

Manufacturing order due dates are scheduled only on work days. Each work day has a production capacity in hours, excluding breaks and non-productive time. Manufacturing operations can only be scheduled up to the production capacity of the day.

You can specify exceptions for overtime or machine downtime. This information is used only when operation schedules are prepared, not when calculating manufacturing order due dates. When a discrepancy occurs, you may have to adjust the due date.

To implement shop calendars correctly:

- Create a calendar with Site, Work Center, and Machine left blank
 - This is the system calendar
- Create a calendar for each site with the Work Center and Machine left blank

- This is the calendar used by CRP to calculate capacity, including holidays
- Create Work Center calendars with site and work center filled in

QAD Enterprise Applications looks first for a calendar for the specific site, work center, machine combination.

- If none is found, it looks for a match on Site and Work Center with Machine = Blank
- If none is found, it looks for a match on Site with both Work Center and Machine = Blank
- If none is found, it looks for a default calendar with Site, Work Center, Machine = Blank


To schedule exceptions, enter the Reference and specify the number of hours per day (positive for overtime, negative for downtime or holidays).

Example If you normally work 8 hours a day, enter -8 hours for a shutdown date.


Use Start and End dates to schedule multiple days of overtime or downtime.

Warning When scheduling overtime, you could schedule a non-work day. When scheduling downtime, each of the days from Start through End must have at least this number of hours normally scheduled, or you could end up with a negative production capacity on those days.

Holiday Maintenance


Our Passion. Your Advantage.

Holiday Maintenance



Site	Date	Day	Holiday
10-100	12/25/2010	Saturday	Christmas Holiday
10-100	12/31/2010	Friday	New Years Eve

Holiday Maintenance (36.2.1)

QAD Proprietary
MS-SU-180

Holidays are days that no one works; the plant is shut down and no production is scheduled. Holidays can be different at each site.

Manufacturing orders are never due and operations are never scheduled on a holiday (you can override this, if desired.)

If a holiday doesn't apply to all work centers, it isn't a holiday. It is an exception to the normal shop calendar. Exceptions are entered using Calendar Maintenance (36.2.5), recording the day off only for the work centers to which it applies.

Rough-Cut Capacity Planning



Rough-Cut Capacity Planning

Examples of Resources

- ▲ Electricity
- ▲ Storage
- ▲ Labor
- ▲ Water

QAD Proprietary

MS-SU-190

Rough-cut capacity planning:

- Shows consumption of critical resources
- Enables master schedulers to:
 - Test end-item production plans
 - Calculate capacity to meet the master schedule
 - Compare and modify required and planned capacity
 - Analyze load on key resources by time period
 - Isolate and resolve potential problems

Resource Maintenance



Master Schedule and RCCP Setup



- ▲ Simulated Forecasting
- ▲ Item and Item-Site Planning Maintenance
- ▲ MRP Control
- ▲ Holiday/Calendar Maintenance
- ▲ Resource Maintenance
- ▲ Item Resource Bill Maintenance

Resource Maintenance

Resource Maintenance

Unit of Measure: HR

Resource: UTS ASSY Site: 10-100

Description: Ultrasound Assembly

Unit of Measure: HR

Reference	Start	End Date	Cap/Day
Normal	10/25/2010		65.0
Downtime	12/24/2010	1/3/2011	-40.0
Seasonal	5/1/2010	8/1/2010	20.0

References allow exact accounting of specific resources over specific time periods

QAD Proprietary MS-SU-210

Resources must be defined before you can evaluate resource load.

Product line planning, master scheduling, and operations planning activities are feasible only if key resources are available. Rough-cut resource planning is usually done prior to committing production resources to a plan.

First, identify the resources in your company that are bottlenecks or can't be easily increased in the short term. These are your key resources. Examples of key resources include specialized labor, special machinery, and cash.

- Define key resources in Resource Maintenance (21.1), then set up resource bills for:
 - Individual product lines in PL Resource Bill Maintenance (21.5)
 - Items in Item Resource Bill Maintenance (21.17)

Load Profiles

Resource bills (also called load profiles) help you compare the resource capacity needed for production against the available capacity. If you need more of any resource than you have available, you must change the plan or increase the resource capacity.

Resource capacity changes over time. For example, another machine or shift is added, or downtime and holidays are scheduled. These changes are recorded with a reference code, start date and end date.

Cap/Day can be positive or negative. If the normal capacity for a resource is 100 hours per day, and you are planning a shutdown on May 10 and 11, you would enter it as:

- Reference [Shutdown]
- Start Date [May 10]
- End Date [May 11] and
- Cap/Day [-100]

A resource's capacity on a specific date is the cumulative capacity from the references which are in effect on that date.

Description. A short description of this resource

- Description prints on most reports and inquiries, as space permits

When you access Help from the Resource field, a pop-up window displays the resource codes and descriptions. You can search through this window in sequence by either field or description. This may influence how you set up your descriptions. For example, you may choose to make the first few characters or words significant for searching purposes.

Reference. This optional code identifies a level of resource capacity, such as:

- Normal
- Vacation
- Shutdown

If you use QAD Enterprise Applications Enterprise Ops Plan, you can access the capacity information for this time period on item resource bills that reference this code. Otherwise, the reference merely describes the resource capacity level for the specified time period.

The capacity of each resource is stated in terms of an average level per day over a certain time period. The capacity may change, perhaps for vacation plant shutdowns or adding a second shift. These capacity changes are identified by reference. The total capacity on any given day is the sum of the capacity components effective on that day.

Example A machine resource has the following capacity levels:

- NORMAL Jan 1 to Dec 31 7 hrs/day
- SHUTDOWN Aug 1 to Aug 31 -7 hrs/day
- 2nd SHIFT Oct 1 to Dec 31 7 hrs/day

The total capacity on August 15th is zero, while the total capacity on October 15th is 14 hours per day.

Key Resource

A single resource can consist of multiple positive or negative dated components.

RCCP tests resources that may limit production of an item's schedule:

- Skilled labor hours
- Production line quantities per hour
- Inspection or testing hours
- Scheduled losses of resource capacity

- Overlapping vacations
- Equipment replacement

Components of a Resource

- Each key resource is defined separately in QAD Enterprise Applications
 - Available in different quantities at different times of the year
- Normal resource quantities are entered as primary resource references or components
- Additional references include the amount by which they add to or subtract from capacity

Example In a firm where five specialized fabricators (such as aluminum welders) are employed, the resource is defined in welder hours. The first component could be defined as the hours that the five employees provide in capacity per day (5 welders x 7 hours = 35 hours/day).

Adding Time-Phased Changes

Additional references can be added for employee's vacations that reduce capacity

- BobV -7.0 hours, July 1 to July 10

Periods of scheduled overtime will increase capacity

- OT 20 hours, September 15 to October 15

When the resource is tested against scheduled production, QAD Enterprise Applications calculates the available resource quantity using these dates and the shop floor calendar.

Item Resource Bill Maintenance



Master Schedule and RCCP Setup



- ▲ Simulated Forecasting
- ▲ Item and Item-Site Planning Maintenance
- ▲ MRP Control
- ▲ Holiday/Calendar Maintenance
- ▲ Resource Maintenance
- ▲ Item Resource Bill Maintenance

Item Resource Bill Maintenance

Item Number: 01010 (2) Site: 10-100

Item Number: 01010

Site: 10-100

Resource: UTS.ASSY

Start Date:

End Date:

Resource Qty Per:

Lead Time (Days):

Offset (Days):

Item Resource Bill Maintenance(21.17)

QAD Proprietary MS-SU-230

Item resource bills are used only to evaluate the manufacturing schedule. Item Resource Bill Maintenance (21.17) records information on resource requirements for individual items.

Manufacturing schedules are feasible only if key resources are available. Rough-cut capacity planning verifies resource availability prior to committing production resources. An item resource bill (or load profile) specifies the amount of a resource required to make one unit of the item. The resource amount is expressed in the resource unit of measure (tons, hours, etc.).

Example To produce a case of ice cream, a blending machine processes 36 kilos of vanilla cream. In the resource record for the blending machine, capacity is expressed in metric tons. Therefore, the resource quantity per for the ice cream item resource bill is 0.036 tons.

The resource bill also determines when and for how long the resource is required.

Lead Time (Days) . Identifies the number of production days the resource is required

Offset (Days). Identifies how many days in advance of production the resource is required

For the ice cream, the blending machine is used for one work day, but the order for the ice cream must be released two days in advance of the requirement.

Note Lead time must always be at least 1 (if zero, no load will be calculated).

Review the Item Resource Load Summary Report (21.22) and Item Resource Load Detail Report (21.24) before committing resources to the production plan.

If you need more of any resource than you have available, you must either change the plan or increase the capacity of the resource.

Creating the End-Item Load

QAD
Our Passion. Your Advantage.

Create the End-Item Load

Master Schedule Order Maint x

Work Order: W0001 ID: 2287245

Item Number: 01010 Medical Ultrasound

Quantity Ordered: 100.0

Quantity Completed: 0.0

Qty Rejected: 0.0

Work Order Status: F

Sales/Job:

Supplier:

Yield Percent: 100.00%

Remarks:

Comments:

Item Resource Bill Maintenance x

Item Number: 01010 (2) Site: 10-100

Resource: UTS ASSY Ultrasound Assembly

Start Date:

End Date:

Resource Qty Per: 0.25

Lead Time (Days): 1

Offset (Days): 0

100 x 0.25 = 25 labor hours required for production

QAD Enterprise Applications multiplies the end item production quantity by the Quantity Per conversion factor to obtain the quantity of resources required.

QAD Proprietary MS-SU-240

QAD Enterprise Applications multiplies the end item production quantity by the Quantity Per conversion factor to obtain the quantity of resources required.

Menu Master Schedule Order Maintenance (22.13)

Menu Item Resource Bill Maintenance (21.17)

Production Conversion Factor

To see exactly how much of a certain resource is required by a scheduled production quantity, the production must be measured in resource units—typically hours or items per day. To do this in QAD Enterprise Applications, determine a conversion factor and enter it in the Resource Qty Per field in Item Resource Bill Maintenance (21.17).

Example To convert production schedules into resource units for RCCP, determine how many hours (or other units) it takes to create a single scheduled end item. If it takes 1.3 hours to complete one end item, the conversion is 1.3. To make 100 end items for the scheduled item, it would take $100 \times 1.3 = 130$ hours.

Lead Times

In order for QAD Enterprise Applications to calculate capacity, at least 1 must be entered in the Lead Time field in Item Resource Bill Maintenance (21.17).

- Lead time is the number of days over which a resource must be available
- A testing process might be required three days after work order release and need two days
 - Offset = -3, Lead Time = 2
- Schedule the first date the resource is required
 - Use work order release dates and number of days the resource is needed
- The Offset is the number of days from work order release that a resource must be available
 - Positive for days before work order release
 - Negative for days following
 - Zero for the same day

Note This method of calculating the offset is the opposite of that used for product structures.



Create the End-Item Load

The screenshot displays two overlapping windows in the QAD software interface:

- Item Planning Maintenance (Top Window):**
 - Item: 01010
 - Item Number: 01010 (2)
 - Supplier:
 - Description: Medical Ultrasound
 - Unit of Measure: EA
- Item Resource Bill Maintenance (Bottom Window):**
 - Item Number: 01010
 - Site: 10-100
 - Resource: UTS ASSY
 - Ultrasound Assembly
 - Run Time: 0.250 (highlighted with a red box)
 - Resource Qty Per: 0.25 (highlighted with a red box)
 - Lead Time (Days): 1
 - Offset (Days): 0
- Right Panel (Item Properties):**
 - Phantom:
 - Minimum Order: 1
 - Maximum Order: 5
 - Order Multiple: 1
 - Op Based Yield:
 - Yield Percent: 100.00%
 - Run Time: 0.250 (highlighted with a red box)
 - Setup Time: 7.500
 - EMT Type: NON-EMT
 - Auto EMT Processing:
 - Network Code: []
 - Routing Code: U-001
 - BOM/Formula: []

Red arrows indicate the flow of information: one arrow points from the 'Run Time' field in the right panel to the 'Run Time' field in the bottom window, and another arrow points from the 'Run Time' field in the bottom window to the 'Resource Qty Per' field in the bottom window.

Exercise: Setup

Enter and Review a Forecast

This activity covers how to enter and review a forecast, and how to set up and observe forecast consumption. Before we do this, however, we will review the items that will be used for the forecasting and master scheduling activities.

- 1 Using Product Structure Inquiry (13.6) to review the parent/component relationship for parent item 01030, and its component items.
- 2 In the Sales Order Control (7.1.24) program, set Ln Format S/M to Single and set Consume Fwd to 1, Consume Back to 2.
- 3 Use Forecast Maintenance (22.1) to enter the following weekly forecast for item 01030 at site 10-100, beginning with the Monday of the next week and covering the following nine weeks

Weeks	Quantity
1	100.0
2	120.0
3	130.0
4	140.0
5	150.0
6	140.0
7	130.0
8	120.0
9	110.0
10	100.0

- 4 Run the Forecast Report (22.4) on both summary and detail for item 01030 only at site 10-100 for the next ten weeks.
- 5 Use Master Schedule Summary Inquiry (22.18) to run the master schedule summary inquiry for 01030 at site 10-100. You should see all ten periods of forecast, plus the forecast simulation distribution.
- 6 Use Sales Order Maintenance (7.1.1) to create a new Sales Order for customer 10C1003.
 - a Make certain that the due date is two weeks from next Monday.
 - b Set Site to 10-100 and Confirmed to Yes.
 - c On order line, enter item 01030 and a quantity of 250.
- 7 Run the Forecast Inquiry (22.3) for 01030 at site 10-100 and review how the forecast has been consumed in the Net Forecast column.
- 8 Run the Master Schedule Summary Inquiry (22.18) and Master Schedule Detail Inquiry (22.21) for 01030, site 10-100 to review the forecast.

Create a Labor Resource

In this activity, create a labor resource and a conversion factor and then compare the labor resource capacities to the load.

- 1 Using Calendar Maintenance (36.2.5), verify there is a shop calendar for site 10-100 (with work center and machine blank). Make sure that Monday through Friday are the established work days and that each day shows eight hours.
- 2 Use Resource Maintenance (21.1) to add labor resources for site 10-100.
 - a to add Labor in the Resource field for site 10-100. Use a description of Labor hours. The unit of measure (UM) is HR for hours.

- b Add the following two references:

Reference	Start	End Date	Cap/Day
Normal	01/01/YY [YY is the current year]	[Blank]	32 [4 assemblers x 8 hours/day]
Downtime	[Four weeks from next Monday]	[Five weeks from next Monday]	32 [4 assemblers x 8 hours/day]

- c Use Resource Browse (21.2) to verify your data are correct. Set the browse to begin at labor.

Add a Family Item

In this activity, we will add a family item in order to forecast and schedule multiple items within the same family.

- 1 Use Item Master Maintenance (1.4.2) to create a family planning item to represent the ultrasound equipment family.

Field	Data
Item Number	01000
Description	Ultrasound equipment
Product Line:	10
Item Type	Family
Status	ACTIVE
Site:	10-100
Master Schedule:	Yes
Plan Orders:	Yes
Order Policy:	POQ
Buyer/Planner:	[your initials]
Pur/Mfg:	F

- 2 Using Product Structure Maintenance (13.5) to create the planning bills for family item 01000. Add parent item 01000 in the product structure and add its components under it:

Component	Description	Quantity	Structure Type	Forecast Percent
01010	Medical Ultrasound	1	P	10%
01020	Implantable Ultrasound	1	P	20%

Component	Description	Quantity	Structure Type	Forecast Percent
01030	Consumer Ultrasound	1	P	30%
01040	Industrial Ultrasound	1	P	40%

- 3 Use Forecast Maintenance (22.1) to enter a forecast for family planning item 01000 at site 10-100; 1000 for each of six weeks, starting with next week.
- 4 View items 01000 and 01010 at site 10-100 in Master Schedule Summary Inquiry (22.18).
- 5 Run Selective MRP (23.3) for items in the range from 01000 to 01040 at site 10-100.
- 6 Review the Master Schedule Summary for items 01000, 01010, 01020, 01030, and 01040. The forecast for the planning item is shown for pegging purposes only. Because its purchase/manufacture code is F, MRP will not plan orders for the planning item.
- 7 Using Sales Order Maintenance (7.1.1), create a sales order in which you sell item 01010 at site 10-100, qty 100, due one week from Monday to customer number 10C1003.
- 8 Run Selective MRP for items in the range from 01000 to 01040 at site 10-100.
- 9 Review the Master Schedule Summary for 01000 and 01010.

Create an Item Resource Bill

In this activity, you create an item resource bill that will be used to determine if the master schedule is achievable.

- 1 Items 01010, 01020, 01030, and 01040 require labor resources. Use Item Resource Bill Maintenance (21.17) to create an Item Resource Bill with the following data:

Item	01010	01020	01030	01040
Site:	10-100	10-100	10-100	10-100
Resource:	Labor	Labor	Labor	Labor
Start Date:	[blank]	[blank]	[blank]	[blank]
End Date:	[blank]	[blank]	[blank]	[blank]
Resource Qty. Per:	4	0.05	0.1	0.2
Lead Time:	2	1	1	1

- 2 Review the Item Resource Load Summary Inquiry (21.21) and Item Resource Load Detail Inquiry (21.23)
 - Has the schedule exceeded capacity in any period?
 - Based on this information, do you think that the plan can be made?

Chapter 4

Using Master Scheduling and RCCP


Course Overview




Use Master Scheduling and RCCP

- ✓ Identify key business considerations before setting up Master Scheduling and RCCP in QAD Enterprise Applications
- ✓ Set up Master Scheduling and RCCP in QAD Enterprise Applications
- ✓ **Use Master Scheduling and RCCP in QAD Enterprise Applications**

Using Master Scheduling and RCCP



Using Master Scheduling and RCCP




- ▲ Master Schedule Order Maintenance
- ▲ Master Schedule Order Browse/Report
- ▲ Sales Order Maintenance (Abnormal Demand)
- ▲ Seasonal Build Maintenance (optional)
- ▲ Seasonal Build Browse/Report (optional)
- ▲ Master Schedule Summary Inquiry/Report
- ▲ Master Schedule Detail Inquiry/Report
- ▲ Selective Materials Plan (optional)
- ▲ Item Resource Load Summary Inquiry/Report
- ▲ Item Resource Load Detail Inquiry/Report


QAD Proprietary MS-PR-030

In this section you learn how to use Master Scheduling and RCCP in QAD Enterprise Applications.

Processing Demand and Supply

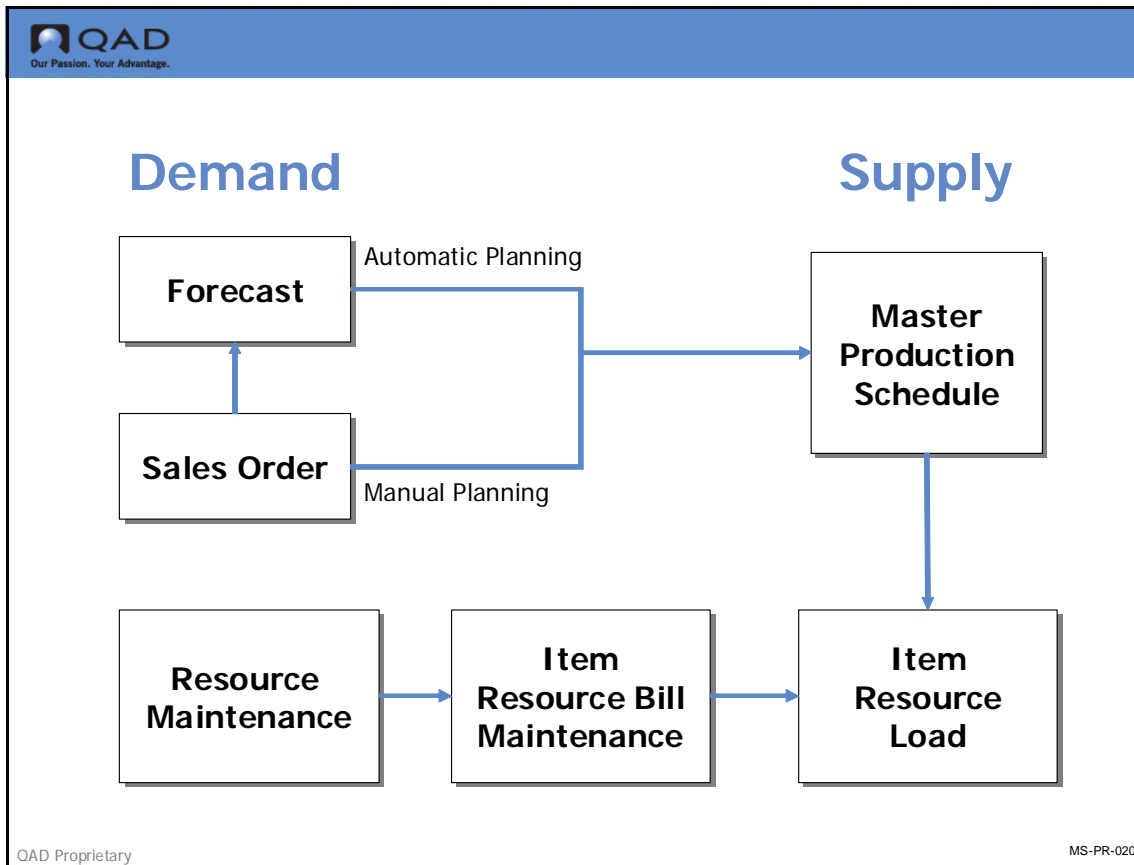

The master scheduler reviews the requirements of the forecast, sales orders, net forecast, seasonal requirements and other demands and creates a master schedule of work orders and or repetitive schedules to satisfy those demands. Rough Cut Capacity Planning is used to ensure the planned master schedule can be done. If it cannot be done adjustments must be made to the master schedule either in the quantities or due dates or both. The master scheduler can use MRP to plan work orders to cover the net forecast or they can create master scheduled work orders manually. Some businesses will use a combination of these techniques for different product lines or in different facilities.

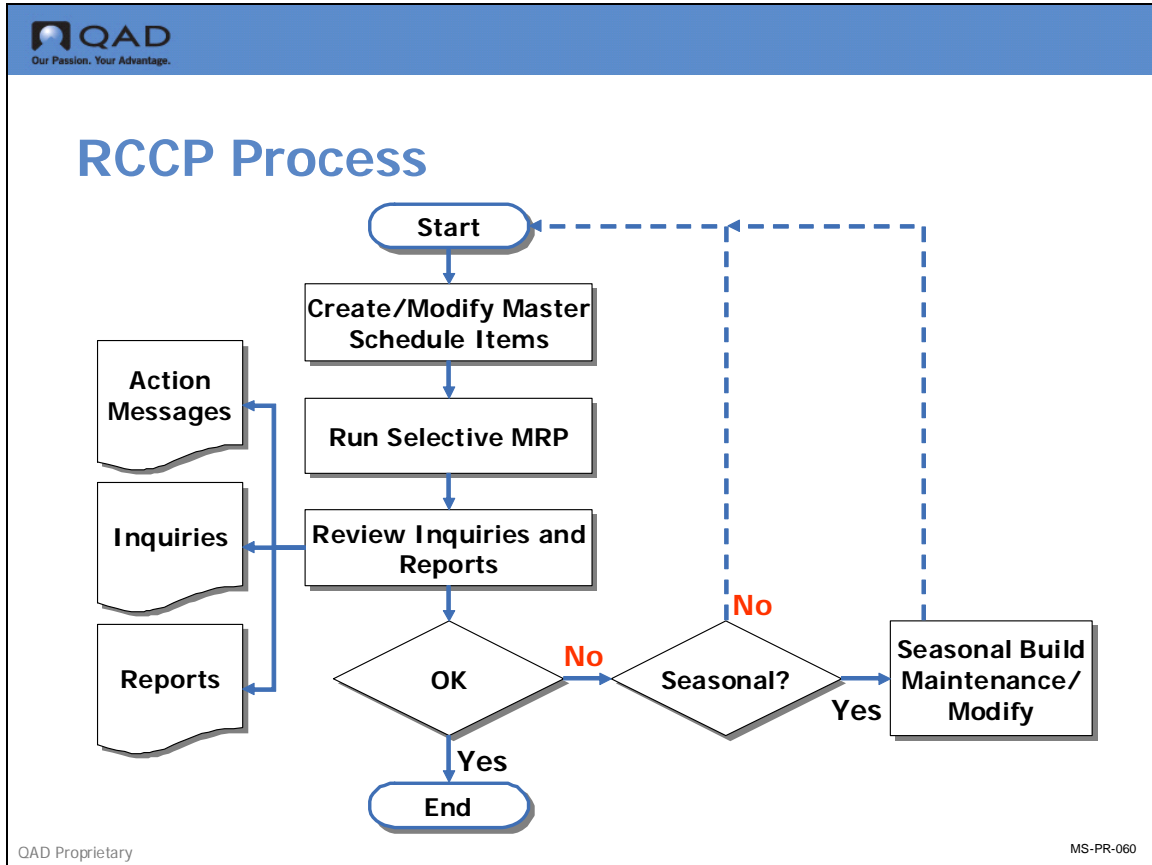

Master scheduling is an iterative process as this diagram shows.

Master Schedule Order Maintenance



Using Master Scheduling and RCCP



- ▲ Master Schedule Order Maintenance
- ▲ Master Schedule Order Browse/Report
- ▲ Sales Order Maintenance (Abnormal Demand)
- ▲ Seasonal Build Maintenance (optional)
- ▲ Seasonal Build Browse/Report (optional)
- ▲ Master Schedule Summary Inquiry/Report
- ▲ Master Schedule Detail Inquiry/Report
- ▲ Selective Materials Plan (optional)
- ▲ Item Resource Load Summary Inquiry/Report
- ▲ Item Resource Load Detail Inquiry/Report

Master Schedule Order Maintenance

Master Schedule Order Maint

Work Order: W0001 ID: 2287245 Site: 10-100

Item Number: 01010 Medical Ultrasound

Type:

Site: 10-100

Quantity Ordered: 100.0 Order Date: 10/26/2010

Quantity Completed: 0.0 Release Date: 10/26/2010

Qty Rejected: 0.0 Due Date: 11/1/2010

Work Order Status: P Site: 10-100

Sales/Job: Routing Code: U-001

Supplier: BOM/Formula Code:

Yield Percent: 100.00%

Remarks:

Comments: Post variances at SFC:

Master Schedule Order Maintenance (22.13)

QAD Proprietary MS-PR-050

Note This screen is the same as Work Order Maintenance (16.1) within the system there is no difference between master schedule work orders and work orders created in the work order module.

To manage the master schedule manually use master schedule order maintenance to create work orders for your master schedule items.

- Enter master schedule orders as firm planned orders
- Master schedule orders are managed and released like normal work orders

To have MRP review master scheduled items and produce action messages, set the following values in Item Planning Maintenance (1.4.7):

Master Schedule. Yes

Plan Orders. No

Order Policy. Any option other than blank


Note These settings insure the system will not create planned orders, but will create action messages about the orders you create.

The firmed supply order creates the master schedule and becomes the primary input to MRP.

The master schedule is controlled by establishing:

- Firmed planned work orders
 - Master Schedule Order Maintenance (22.13)
- Repetitive schedules
 - Schedule Maintenance (18.2.1)
 - Can be used to master schedule items, even if work orders track actual production (this means you have to take the exploded type S work orders from the repetitive schedule and change them to R)
- Purchase requisitions
 - Purchase Requisition Maintenance (5.1.4)

MPS using Forecast Maintenance


Our Passion. Your Advantage.

Forecast Maintenance

Forecast Maintenance x
Go To Actions Copy Print Preview Attach

Item Number: 01010 (2) Site: 10-100

Item Number: Site: Year:

Week	Forecast	Week	Forecast	Week	Forecast	Week	Forecast
1/4/2010	100	4/5/2010	160	7/5/2010	160	10/4/2010	110
1/11/2010	110	4/12/2010	160	7/12/2010	170	10/11/2010	100
1/18/2010	120	4/19/2010	150	7/19/2010	180	10/18/2010	110
1/25/2010	130	4/26/2010	140	7/26/2010	190	10/25/2010	120
2/1/2010	140	5/3/2010	130	8/2/2010	200	11/1/2010	130
2/8/2010	160	5/10/2010	120	8/9/2010	190	11/8/2010	140
2/15/2010	170	5/17/2010	110	8/16/2010	180	11/15/2010	150
2/22/2010	180	5/24/2010	100	8/23/2010	170	11/22/2010	160
3/1/2010	190	5/31/2010	110	8/30/2010	160	11/29/2010	170
3/8/2010	200	6/7/2010	120	9/6/2010	150	12/6/2010	180
3/15/2010	190	6/14/2010	130	9/13/2010	140	12/13/2010	190
3/22/2010	180	6/21/2010	140	9/20/2010	130	12/20/2010	200
3/29/2010	170	6/28/2010	150	9/27/2010	120	12/27/2010	190
Total	2,040	Total	1,720	Total	2,140	Total	1,950

Forecast Maintenance (22.1)

QAD Proprietary
MS-PR-055

MPS may also be loaded using Forecast Maintenance (22.1). This function allows you to enter up to 52 weekly buckets of forecast demand for an item at a site. This demand is seen by MRP and planned orders are created for the net forecast. The master scheduler can then review the plan using the summary and detail inquiries.

To use this functionality, set Item Planning Maintenance (1.4.7) Master Schedule Yes, Planned Orders Yes and a valid Order Policy.

Master Schedule Summary Inquiry

QAD
Our Passion. Your Advantage.

Master Schedule Summary Inquiry

Master Schedule Summary Inq... X

Run | Export to Excel | View as PDF

Item Number: 01010 | Site: 10-100 | Display Negative ATP: | Start Date: 10/25/2010 | End Date: 12/31/2010 | Column Type: Week | Per Column: 1 | Columns: 11

Item Number:	01010	Medical Ultrasound				MRP Required:	Yes
Site:	10-100	Mfg LT:	4	Plan Orders:	Yes	Pur/Mfg:	M
Qty on Hand:	10.0 EA	Purchase LT:	0	Order Quantity:	0	Minimum Order:	1
Order Policy:	POQ	Safety Stock:	0	Yield Percent:	100.00%	Maximum Order:	5
Order Period:	7	Safety Time:	0	Time Fence:	0	Order Multiple:	1

Category	Past	10/25/2010	11/1/2010	11/8/2010	11/15/2010	11/22/2010
Production Forecast	0	0	0	0	0	0
Forecasts	1339	108	130	140	150	
Sales Orders	31	12	0	0	0	
Gross Requirements	0	0	0	0	0	
Master Schedule	282	25	100	0	21	
Projected QOH	-1078	-1173	-1203	-1343	-1472	
Available to Promise	251	23	100	0	0	
Cumulative ATP	251	274	374	374	374	

QAD Proprietary MS-PR-056

Master Schedule Summary and Detail Inquiries/Reports

The Master Schedule Summary Inquiry (22.18) and Report (22.19), are one of the most useful inquiries for the master scheduler to review the overall situation for an item. The inquiry and report both display the following information:

Header Information

The header shows the item, site, start (and or end date) date of the inquiry and whether the buckets are D days, W weeks, M months, or P general ledger period. It also shows how many periods you choose to display in each column. You can display two weeks in each column for example.

The header also shows the quantity on hand the MRP Required flag and all of the item planning data for the site specified.

Production Forecast. System-calculated forecast used in multilevel master scheduling

Forecast. Forecast quantity for an item, either loaded into forecast summary files using Simulation to Summarized Forecast or entered manually using Forecast Maintenance (22.1) or Forecast Worksheet Maintenance (22.2).

Sales Orders. Demand derived from confirmed sales orders and required ship schedules

Gross Requirements. The sum of an item's requirements from forecasts, higher-level products, confirmed sales orders, required ship schedules, service items, and intersite orders generated by DRP. Gross requirements do not take into account inventory on hand or scheduled receipts.

Master Scheduled Receipts. Total scheduled receipts for an item from work orders, repetitive schedules, purchase orders, and distribution orders.

Projected QOH. Projected item quantity on hand, calculated by the system. This is a projection by period of an item's on-hand balance plus scheduled receipts minus gross requirements.

Available-to-Promise. The uncommitted portion of inventory or planned production, calculated by deducting real demand from real supply.

Seasonal Build. For products with seasonal demand cycles, you may need to build up inventory in advance of periods of peak demand.

You can do this using work orders or repetitive schedules, or you can use seasonal build requirements to build up inventory to a predetermined level prior to its expected demand.

Seasonal build requirements let master schedulers specify a target inventory level for seasonal demand items that is not included when calculating ATP quantities, but can still be allocated and shipped on sales orders and customer schedules.

Seasonal build quantities appear separately on master schedule reports that display ATP quantities.

Note The seasonal build heading and quantities only display when there are seasonal build requirements.

The Master Schedule Detail Inquiry (22.21) and Report (22.22) functions display the same information as the Master Schedule Summary Inquiry (22.18) and Report (22.19), sequenced by due date.

They also include source-to-demand pegging details, allowing you to identify the actual work order or sales order generating a particular item requirement.

Master Schedule Detail Inquiry

QAD
Our Passion. Your Advantage.

Master Schedule Detail Inquiry

Master Schedule Detail Inquiry

10/26/10

Item Number: 01010	Site: 10-100	Start Date: 10/25/10
Medical Ultrasound		Output: PAGE
Item Number: 01010	Qty on Hand: 10.0	Site: 10-100
Medical Ultrasound	UM: EA	Pur/Mfg: M
Buyer/Planner: 1-01	Order Policy: POQ	Min Order: 1
Mstr Sched: Yes	Order Period: 7	Max Order: 5
MRP Required: Yes	Time Fence: 0	Ord Mult: 1
Plan Orders: Yes	Safety Time: 0	Order Qty: 0
Issue Policy: Yes	Safety Stock: 0	Yield Percent: 100.00%
		Cum LT: 0

Due Date	Gross Reqs	Mstr Sched	Proj QOH	Plan Ords	Details
10/25/10			-1,115		Beginning Available
10/25/10	108		-1,186		Forecast
10/25/10	2		-1,188		S0: S0101004 Line: 1
10/25/10	2		-1,190		S0: S0101007 Line: 1
10/25/10	1		-1,191		S0: S0101010 Line: 1
10/25/10	1		-1,192		S0: S0101010 Line: 5
10/25/10	1		-1,193		S0: S0101013 Line: 1
10/25/10	1		-1,194		S0: S0101013 Line: 5
10/25/10	2		-1,196		S0: S0101017 Line: 1
10/25/10	2		-1,198		S0: S0101017 Line: 3
10/25/10			-1,173	25	W/O: 08020012 ID: 2286315
11/01/10	130		-1,303		Release Date 10/19/10
11/01/10			-1,203	100	Forecast W/O: W0001 ID: 2287245
11/08/10	140		-1,343		Release Date 10/26/10
11/15/10	150		-1,493		Forecast
11/21/10			-1,472	21	Forecast W/O: 1110028 ID: 2283017
11/22/10	139		-1,611		Release Date 11/20/10
11/25/10	4		-1,615		Forecast
11/25/10	4		-1,619		S0: S0111004 Line: 1
11/25/10	2		-1,621		S0: S0111007 Line: 1
					S0: S0111010 Line: 1

QAD Proprietary
MS-PR-057

The Master Schedule Detail Inquiry (22.21) provides a very different view of the MPS item. This view shows in a vertical list format each transaction, by date, that effects the item at this site. The display also shows detail information about both the source of the demand and the supply.

In this example we see the demand is from a production forecast for a higher level planning item. We also see the system has planned an MRP W/O to satisfy that demand, and its release date. Once the work orders are firm (approved) or released the quantity will move into the Master Schedule column.

As with the summary inquiry the header shows the item planning data.

Master Schedule Order Browse/Report




Using Master Scheduling and RCCP



- ▲ Master Schedule Order Maintenance
- ▲ Master Schedule Order Browse/Report
- ▲ Sales Order Maintenance (Abnormal Demand)
- ▲ Seasonal Build Maintenance (optional)
- ▲ Seasonal Build Browse/Report (optional)
- ▲ Master Schedule Summary Inquiry/Report
- ▲ Master Schedule Detail Inquiry/Report
- ▲ Selective Materials Plan (optional)
- ▲ Item Resource Load Summary Inquiry/Report
- ▲ Item Resource Load Detail Inquiry/Report

Master Schedule Order Browse


Our Passion. Your Advantage.

Master Schedule Order Browse

Master Schedule Order Browse

Print
Add to Favorites
Chart
Chart Designer
Refresh
New
Edit

Search

starts at

Viewing 1 - 100 of 401
Records per page: 100

Item Number	Release Date	Work Order ID	Quantity Open	Due Date	Sales/Job	Work Order Status
01010	07/14/2010	0510028	2281184	0.0	05/21/2010	C
01010	07/19/2010	0610028	2281534	0.0	06/21/2010	C
01010	07/24/2010	0710028	2282027	0.0	07/21/2010	C
01010	08/10/2010	08020002	2286305	12.0	08/16/2010	P
01010	08/20/2010	0810028	2282408	12.0	08/21/2010	F
01010	08/17/2010	08020003	2286306	25.0	08/23/2010	P
01010	08/24/2010	08020004	2286307	25.0	08/30/2010	P
01010	08/31/2010	08020005	2286308	25.0	09/06/2010	P
01010	09/07/2010	08020006	2286309	25.0	09/13/2010	P
01010	09/14/2010	08020007	2286310	25.0	09/20/2010	P
01010	09/20/2010	0910028	2282625	21.0	09/21/2010	F


Master Schedule Order Browse (22.14)

QAD Proprietary
MS-PR-080

Status.


- F = Firm
- P = Planned

Master Schedule Order Report


Our Passion. Your Advantage.

Master Schedule Order Report

Master Schedule Order Report... X
10/26/10




Master Schedule Order Report
10USA


Work Order	ID	Item Number	Qty Ordered	Open Qty	UM	Order Date	Rel Date	Due Date	SO/Job	ST
08020111	2286399	60003 Keyboard	25.0	25.0	EA	08/02/10	08/12/10	08/17/10		P
08020112	2286400	60003 Keyboard	40.0	40.0	EA	08/02/10	08/19/10	08/24/10		P
08020113	2286401	60003 Keyboard	40.0	40.0	EA	08/02/10	08/26/10	08/31/10		P
08020114	2286402	60003 Keyboard	40.0	40.0	EA	08/02/10	09/02/10	09/07/10		P
08020115	2286403	60003 Keyboard	61.0	61.0	EA	08/02/10	09/09/10	09/14/10		P
08020116	2286404	60003 Keyboard	40.0	40.0	EA	08/02/10	09/16/10	09/21/10		P
08020117	2286405	60003 Keyboard	40.0	40.0	EA	08/02/10	09/23/10	09/28/10		P
08020118	2286406	60003 Keyboard	40.0	40.0	EA	08/02/10	09/30/10	10/05/10		P
08020119	2286407	60003 Keyboard	40.0	40.0	EA	08/02/10	10/07/10	10/12/10		P
08020120	2286408	60003 Keyboard	52.0	52.0	EA	08/02/10	10/14/10	10/19/10		P
08020131	2286419	60006 Monitor Cable	22.0	22.0	EA	08/02/10	10/01/10	10/05/10		P
08020132	2286420	60006 Monitor Cable	25.0	25.0	EA	08/02/10	10/08/10	10/12/10		P
08020133	2286421	60006 Monitor Cable	37.0	37.0	EA	08/02/10	10/15/10	10/19/10		P
08020140	2286428	60013 Probe Unit Sealed Unit	45.0	45.0	EA	08/02/10	07/28/10	08/02/10		P
08020141	2286429	60013 Probe Unit Sealed Unit	25.0	25.0	EA	08/02/10	08/13/10	08/19/10		P

QAD Proprietary
MS-PR-090

Sales Order Maintenance - Abnormal Demand



Using Master Scheduling and RCCP



- ▲ Master Schedule Order Maintenance
- ▲ Master Schedule Order Browse/Report
- ▲ Sales Order Maintenance (Abnormal Demand)
- ▲ Seasonal Build Maintenance (optional)
- ▲ Seasonal Build Browse/Report (optional)
- ▲ Master Schedule Summary Inquiry/Report
- ▲ Master Schedule Detail Inquiry/Report
- ▲ Selective Materials Plan (optional)
- ▲ Item Resource Load Summary Inquiry/Report
- ▲ Item Resource Load Detail Inquiry/Report

QAD Proprietary MS-PR-100

Abnormal demand is usually a large, unexpected sale.

Sales Order Maintenance - Abnormal Demand

Sales Order Maintenance – Abnormal Demand

Sales Order Maintenance X

Go To Actions Copy Print Preview Attach

Attachments

Header Lines Trailer

Lines Line Details Freight Data Tax Info Comments

Header

Order: S0001 Sold-To: 10-300 Ln For: Single

Sales Order Line

Ln	Item Number	Qty Ordered	UM	List Price	Discount	Net Price
1	01010	1,000.0	EA	500.00	0.0	500.00

Line Details

Desc: CONTROL UNIT, AUTOMOTIVE Sales Acct: 4010 mech ADM

Loc: 010 Site: 10-100 Disc Acct: 4200 Mech

USD Cost: 46.66688 Confirmed: Credit Terms Int: 0.00

Lot/Serial: Qty Allocated: 0.0 Required: 11/19/2008 Ship Type:

Qty Picked: 0.0 Promised: 11/18/2008 UM Conversion: 1.0000

Qty Shipped: 0.0 Due Date: 10/23/2008 Consume Fcst:

Qty to Invoice: 0.0 Perform Date: Pricing Date: 10/22/2008 Detail Alloc:

Salesperson 1: Multiple: Fixed Price: Taxable: Freight List: 10FRT

Commission 1: 10.00% Category: Comments:

QAD Proprietary Sales Order Maintenance (7.1.1) MS-PR-110

There are circumstances where the master scheduler may not want forecast consumption to occur. This would be the case when an unexpected sales order is received, which was not part of the forecast and should not be considered for the next year's forecast.

To indicate a sales order as Abnormal Demand in QAD Enterprise Applications, set:

- Consume Forecast = No in Sales Order Maintenance (7.1.1)

MRP will now plan this independent demand requirement without consuming forecasts for the period.

Some Causes of Abnormal Demand

- Unplanned orders received due to:
 - Hurricanes
 - Earthquakes
 - Floods
 - New customers
 - New markets
- These types of orders generally do not apply to forecasts

In the case of new customers and new markets a decision needs to be made whether these reflect ongoing business in which case you will want to adjust the forecast to take them into account.

Forecast Worksheet Maintenance

QAD
Our Passion. Your Advantage.

Forecast Worksheet Maintenance

Forecast Worksheet Maintena... X
Go To ▾ Action ▾

Item Number: 01010
Site: 10-100
Year: 2010

Week	Forecast	Sales	Abnormal	Prod Fcst	Net Forecast
40	10/01/2007	0	0	0	0
41	10/08/2007	0	0	0	0
42	10/15/2007	0	0	0	0
43	10/22/2007	0	0	0	0
44	10/29/2007	0	0	0	0
45	11/05/2007	100	0	0	100
46	11/12/2007	120	0	600	120
47	11/19/2007	130	0	600	20
48	11/26/2007	140	250	600	0
49	12/03/2007	130	0	600	130
50	12/10/2007	120	0	1,000	120
51	12/17/2007	110	0	600	110
52	12/24/2007	120	0	0	120
Totals		970	250	1,000	720

Forecast Worksheet Maintenance (22.2)

QAD Proprietary
MS-PR-115

Forecast Worksheet Maintenance (22.2) shows 13 weeks per frame and cycles through however much data you have entered. It is a very useful screen in that it displays the current forecast, actual sales by period, abnormal sales, the production forecast and the net forecast. In addition it is a maintenance screen so you can modify the forecast as required.


In the screen above note that the sale in period 48 has consumed the forecast in the current period and gone back a period to consume the balance of the sale as specified in the consume forward and back logic in Sales Order Control (7.1.24).

The abnormal sale in period 50 has not consumed the forecast. The sale order flag “consume forecast” was unchecked on this sale order.


The production forecast comes from the forecast for the family item we setup earlier and is showing how many of this item are required based on the percent distribution of the family.

It is very helpful for the master scheduler to understand the sources of demand for the various items. The master scheduler might also detect on this screen a very large sales order that was consuming forecast when it should not because someone failed to mark it a “consume forecast No.”

Seasonal Build Maintenance



Using Master Scheduling and RCCP



- ▲ Master Schedule Order Maintenance
- ▲ Master Schedule Order Browse/Report
- ▲ Sales Order Maintenance (Abnormal Demand)
- ▲ Seasonal Build Maintenance (optional)
- ▲ Seasonal Build Browse/Report (optional)
- ▲ Master Schedule Summary Inquiry/Report
- ▲ Master Schedule Detail Inquiry/Report
- ▲ Selective Materials Plan (optional)
- ▲ Item Resource Load Summary Inquiry/Report
- ▲ Item Resource Load Detail Inquiry/Report

QAD Proprietary MS-PR-120

This program allows incremental buildup and release of inventory. At times, the master scheduler may need incremental inventory build up to a predetermined level. This situation most often occurs for seasonal demand items.

- Need to build up an item's inventory prior to its expected demand
- Input into the master schedule is required

Although master scheduled orders could be entered to adjust for seasonality, identifying a demand as seasonal build prevents MRP from issuing action messages to cancel or delay orders for those items whose demand is not yet apparent.

The screenshot displays the 'Seasonal Build Maintenance' window for Item Number 01010 (Medical Ultrasound) at Site 10-100. The window shows four sequential screens, each representing a different date and the corresponding seasonal inventory level. The inventory levels are 200.0, 400.0, 600.0, and 0.0, respectively. The reference is 'INTRO' and the unit of measure is 'EA'.

Date	Seasonal Inventory	UM
11/3/2010	200.0	EA
11/10/2010	400.0	EA
11/17/2010	600.0	EA
11/24/2010	0.0	EA

QAD Proprietary Seasonal Build Maintenance (22.9) MS-PR-130

In this example 600 units are needed over and above forecast to support a product launch. It is desired to build them at the rate of 200 units per week for the next three weeks. The seasonal build is setup as shown in the following screens.

In QAD Enterprise Applications, seasonal build inventory is entered into the system using Seasonal Build Maintenance (22.9). At the end of the first build week there will be 200 units in inventory.

At the end of the second build week there will be 400 units in inventory.

At the end of the third build week there will be 600 units in inventory.

At the end of the fourth week we set the seasonal inventory to zero. This releases the 600 units to be available.

Seasonal Build Browse/Report




Using Master Scheduling and RCCP



- ▲ Master Schedule Order Maintenance
- ▲ Master Schedule Order Browse/Report
- ▲ Sales Order Maintenance (Abnormal Demand)
- ▲ Seasonal Build Maintenance (optional)
- ▲ Seasonal Build Browse/Report (optional)
- ▲ Master Schedule Summary Inquiry/Report
- ▲ Master Schedule Detail Inquiry/Report
- ▲ Selective Materials Plan (optional)
- ▲ Item Resource Load Summary Inquiry/Report
- ▲ Item Resource Load Detail Inquiry/Report

Seasonal Build Browse


Our Passion. Your Advantage.

Seasonal Build Inquiry – Optional

Seasonal Build Browse

Print
Add to Favorites
Chart
Chart Designer
Refresh
New
Edit

Search

Item Number starts at

Viewing 1 - 4 of 4 Records per page: 100

Item Number	Site	Date	Reference	Seasonal Inventory	Unit of Measure	Description
01010	10-100	11/03/2010	INTRO	200.0	EA	Medical Ultrasound
01010	10-100	11/10/2010	INTRO	400.0	EA	Medical Ultrasound
01010	10-100	11/17/2010	INTRO	600.0	EA	Medical Ultrasound
01010	10-100	11/24/2010	INTRO	0.0	EA	Medical Ultrasound

Seasonal Build Inquiry (22.10)

QAD Proprietary
MS-PR-150

The Seasonal Build Browse (22.10) shown above illustrates a completed seasonal build.

Master Schedule Summary Inquiry/Report



Using Master Scheduling and RCCP



- ▲ Master Schedule Order Maintenance
- ▲ Master Schedule Order Browse/Report
- ▲ Sales Order Maintenance (Abnormal Demand)
- ▲ Seasonal Build Maintenance (optional)
- ▲ Seasonal Build Browse/Report (optional)
- ▲ Master Schedule Summary Inquiry/Report
- ▲ Master Schedule Detail Inquiry/Report
- ▲ Selective Materials Plan (optional)
- ▲ Item Resource Load Summary Inquiry/Report
- ▲ Item Resource Load Detail Inquiry/Report

Master Schedule Summary Inquiry

Category	Past	10/25/2010	11/1/2010	11/8/2010	11/15/2010	11/22/2010
Production Forecast	0	0	0	0	0	0
Forecasts	899	0	0	0	0	0
Sales Orders	31	1012	0	0	0	0
Gross Requirements	0	0	0	0	0	0
Master Schedule	282	25	100	0	21	0
Projected QOH	-638	-1625	-1525	-1525	-1504	-1483
Available to Promise	0	-626	0	0	0	0
Cumulative ATP	0	-626	-626	-626	-626	-626

The master schedule summary is the single most crucial screen for planners to understand. It highlights:

Production forecast

- System calculated forecast used in multilevel master scheduling

Forecast

- Manually loaded or via Simulation to Summarized Forecast
 - Independent demand entered in Forecast Maintenance

Sales orders

- Demand derived from sales orders, required ship schedules
 - Independent demand entered in Sales Order Maintenance

Gross requirements

The sum of an item's requirements from:

- Forecasts
- Higher level products
- Confirmed sales orders

- Required ship schedules
- Service items
- Intersite orders generated by DRP

Gross requirements do not take into account inventory on hand or scheduled receipts.

- Manufacturing requirements from a parent work order
 - Can be both master scheduled and a component on a multilevel bill
 - May be intersite demand in DRP environment

Master Scheduled Receipts

Total scheduled receipts for an item from:

- Work orders
- Repetitive schedules
- Master schedule orders
- Purchase orders
- Distribution orders

Projected quantity on hand (QOH)

- System calculated
- A period-by-period projection of an item's on-hand balance plus scheduled receipts minus gross requirements

Available-to-Promise

The uncommitted portion of inventory or planned production calculated by deducting real demand from real supply.

Seasonal Build

Quantity in inventory for that period NOT INCLUDED in available-to-promise quantity.

Available-to-Promise Calculation (QAD Enterprise Applications methodology)

- Beginning QOH
 - + Master schedule receipts
 - - Gross requirements
 - - Sales (until next master schedule)
 - - Increased seasonal build
 - + Decreased seasonal build

Order Promising

QAD
Our Passion. Your Advantage.

Master Schedule Summary Inquiry

Master Schedule Summary Inq... x

Run | Export to Excel | View as PDF

Item Number: 01010 | Site: 10-100 | Display Negative ATP: | Start Date: 10/25/2010 | End Date: | Column Type: Week | Per Column: 1 | Columns: 12

Item Number: 01011 Medical Ultrasound | MRP Required: Yes
 Site: 10-100 | Mfg LT: 4 | Plan Orders: Yes | Pur/Mfg: M
 Qty on Hand: 10.0 EA | Purchase LT: 0 | Order Quantity: 0 | Minimum Order: 1
 Order Policy: POQ | Safety Stock: 0 | Yield Percent: 100.00% | Maximum Order: 5
 Order Period: 7 | Safety Time: 0 | Time Fence: 0 | Order Multiple: 1

Category	Past	10/27/2010	11/3/2010	11/10/2010	11/17/2010	11/24/2010
Production Forecast	0	0	0	0	0	0
Forecasts	0	0	0	0	0	0
Sales Orders	0	0	0	500	0	0
Gross Requirements	0	0	0	0	0	0
Master Schedule	0	0	0	0	0	0
Projected QOH	0	0	0	-500	-500	0
Available to Promise	0	-500	0	0	0	0
Cumulative ATP	0	-500	-500	-500	-500	-500

QAD Proprietary MS-PR-190

The completed master schedule provides a basis for order promising. Order promising simply verifies whether a sales order can be filled within a specific time frame given other demands and the currently scheduled supply orders.

Available-to-Promise (ATP)

- Shows true day-to-day supply available to fulfill incoming sales orders
- Order promising verifies whether a sales order can be filled within a specific time frame
 - Check Avail Promise row of the Master Schedule Summary Inquiry (22.18)
- Tracks real supply against real demand
- Does not factor in Forecast or Prod Forecast quantities
- Does factor in Seasonal Build
 - Increase in Seasonal Build decreases ATP
 - Decrease in Seasonal Build increases ATP

The calculation occurs on any date when a Master Sched receipt is due or a Seasonal Build quantity is made available and a net increase in supply is caused.

- Includes all sales orders and gross requirements up to the next increase in available supply

Calculation

Master Sched – Sales Orders – Gross Requirements – Seasonal Build net increases + Seasonal Build net decreases = Available-to-Promise

Warning Sales orders can use ATP from the past, which can be confusing when interpreting the calculation.

This is true except in the first instance of available-to-promise on a summary screen.

To start the ATP out, the beginning quantity on hand is added.

In the Past columns of the daily Master Schedule Summary (as well as in the weekly and monthly displays), ATP is Time Period sensitive (Net Amount):

- All uncommitted supply that can be promised to new sales orders is shown
- The ATP is decremented during sales order entry and is revised immediately

Cumulative Available-to-Promise (ATP)

Classic ATP only calculates a value in the first period if there is on hand balance or in any period with a master schedule order due. Using this rule the second period above does not have an ATP value. In Cumulative ATP an unconsumed portion of a periods ATP may be carried forward until it is consumed. Using this rule the second period has ATP carried forward from the first period.

Master Schedule Summary Report

QAD
Our Passion. Your Advantage.

Master Schedule Summary Report

Master Schedule Summary Report
Training

10/28/08 20:36:13
Page: 1

Item Number: 01010	Medical Ultrasound	Buyer/Planner:	Site: 10-100
Prod Line: 10	BOM/Formula Code:	Supplier:	
Qty on Hand: 10.0	UM: EA	Time Fence: 0	Manufacturing Lead Time: 0
Order Policy: PQQ	Minimum Order: 0	Safety Time: 0	Pur/Mfg: M
Order Period: 7	Maximum Order: 0	Safety Stk: 0	Inspect: No
Order Qty: 0	Ord Mult: 0	Yield%: 100.00%	Cumulative Lead Time: 0

Past	10/27/08	11/03/08	11/10/08	11/17/08	11/24/08	12/01/08	12/08/08	12/15/08	12/22/08	12/29/08	01/05/09	01/12/09
	10/26/08	11/02/08	11/09/08	11/16/08	11/23/08	11/30/08	12/07/08	12/14/08	12/21/08	12/28/08	01/04/09	01/11/09
Prod Fcst	0	0	0	0	0	0	0	0	0	0	0	0
Forecast	0	0	0	0	0	0	0	0	0	0	0	0
Sales Orders	0	0	0	500	0	0	0	0	0	0	0	0
Gross Reqs	0	0	0	0	0	0	0	0	0	0	0	0
Mstr Sched	0	0	0	0	0	0	0	0	0	0	0	0
Projected QOH	0	0	0	-500	-500	-500	-500	-500	-500	-500	-500	-500
Avail Promise	0	-500	0	0	0	0	0	0	0	0	0	0
Cum ATP	0	-500	-500	-500	-500	-500	-500	-500	-500	-500	-500	-500

Master Schedule Summary Report (22.19)

QAD Proprietary
MS-PR-200


The inquiry is always for a single item at a single site. You can specify a start and end date and the bucket type and number of bucket periods per column.

The report


- Provides a printed copy of the Master Schedule Summary Inquiry
- Gives costing data of the quantitative data displayed

While the data displayed on the MPS summary report (shown above) is the same as the MPS summary inquiry (previous page). The selection screen offers considerably more flexibility than the inquiry.

Master Schedule Summary Report


Our Passion. Your Advantage.

Master Schedule Summary Report

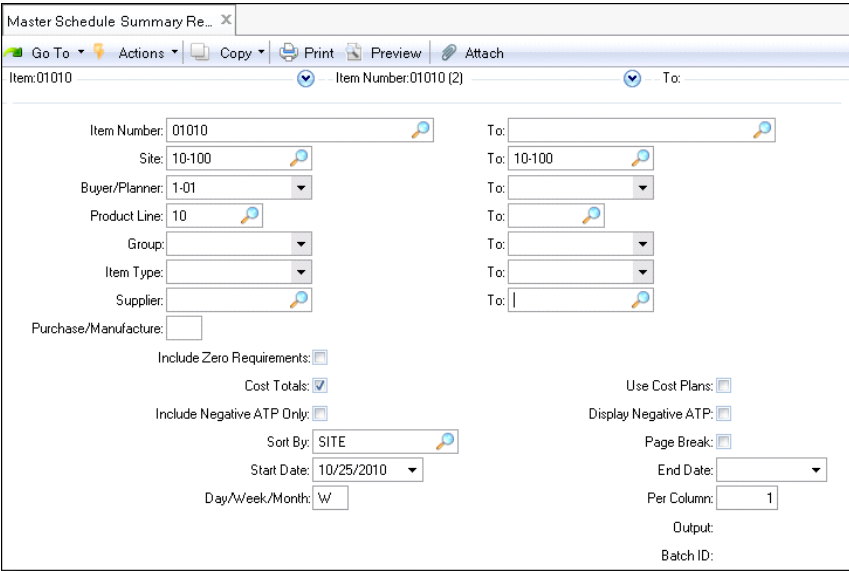

Master Schedule Summary Report (22.19)

QAD Proprietary
MS-PR-205

The report allows a broad range of selection criteria. Whether printed to paper or viewed on the terminal, this report gives the master scheduler a powerful tool for reviewing the schedule.

Master Schedule Detail Inquiry/Report



Using Master Scheduling and RCCP



- ▲ Master Schedule Order Maintenance
- ▲ Master Schedule Order Browse/Report
- ▲ Sales Order Maintenance (Abnormal Demand)
- ▲ Seasonal Build Maintenance (optional)
- ▲ Seasonal Build Browse/Report (optional)
- ▲ Master Schedule Summary Inquiry/Report
- ▲ Master Schedule Detail Inquiry/Report
- ▲ Selective Materials Plan (optional)
- ▲ Item Resource Load Summary Inquiry/Report
- ▲ Item Resource Load Detail Inquiry/Report

Master Schedule Detail Inquiry

QAD
Our Passion. Your Advantage.

Master Schedule Detail Inquiry

QAD Master Schedule Detail Inquiry 10/28/08

Item Number: 01010 Site: 10-100 Start Date: 11/03/08
 Medical Ultrasound Output: page

Item Number: 01010 Qty on Hand: 0.0 Site: 10-100
 Medical Ultrasound UM: EA Pur/Mfg: M
 Buyer/Planner: 1-01 Order Policy: POQ Min Order: 0 Mfg LT: 0
 Mstr Sched: Yes Order Period: 7 Max Order: 0 Pur LT: 0
 MRP Required: Yes Time Fence: 0 Ord Mult: 0 Ins LT: 0
 Plan Orders: Yes Safety Time: 0 Order Qty: 0 Inspect: No
 Issue Policy: Yes Safety Stock: 0 Yield Percent: 100.00% Cum LT: 0

Due Date	Gross Reqs	Mstr Sched	Proj QOH	Plan Ords	Details
11/03/08			0		Beginning Available
11/10/08	500		-500		SO: S0123456 Line: 1

List complete

22.21 Master Schedule Detail Inquiry mmsiq01.p

Master Schedule Detail Inquiry (22.21)

QAD Proprietary MS-PR-220


The Master Schedule Detail Inquiry displays:

- A date-sequenced description of each demand and supply record
- Item/site planning data followed by a time-phased replenishment display in due date sequence

The screen shows the same information as the Master Schedule Summary Inquiry, including the pegging of demands to their source. For example, the actual work order or sales order that generated the requirement is identified.

Note One-level pegging is available in QAD Enterprise Applications

Master Schedule Detail Report



Master Schedule Detail Report

Training

10/28/08 20:48:17

Page:1

Item Number: 01010
 Prod Line: 10
 Qty on Hand: 10.0
 Order Policy: PQQ
 Order Period: 7
 Order Qty: 0

Medical Ultrasound
 UM: EA
 Minimum Order: 0
 Maximum Order: 0
 Ord Mult: 0

BOM/Formula Code:
 Time Fence: 0
 Safety Time: 0
 Safety Stk: 0
 Yield%: 100.00%

Buyer/Planner:
 Supplier:
 Manufacturing Lead Time: 0
 Pur/Mfg: M Purchase LT: 0
 Inspect: No Inspect LT: 0
 Cumulative Lead Time: 0

Site: 10-100
 MRP Required: Yes
 Mstr Sched: Yes
 Plan Orders: Yes
 Issue Policy: Yes

Date	Gross Reqmt	Master Schedule	Projected Qty OH	Planned Order(Due)	Details
10/27/08	120.0		-120.0		Forecast
10/28/08			0.0	120.0	W/O: 10280002 ID: 406059 Release Date 10/25/08
11/03/08	130.0		-130.0		Forecast
11/03/08			0.0	130.0	W/O: 10280003 ID: 406060 Release Date 10/31/08
11/10/08	140.0		-140.0		Forecast
11/10/08			0.0	140.0	W/O: 10280004 ID: 406061 Release Date 11/07/08
11/17/08	150.0		-150.0		Forecast
11/17/08			0.0	150.0	W/O: 10280005 ID: 406062 Release Date 11/14/08
11/24/08	140.0		-140.0		Forecast
11/24/08			0.0	140.0	W/O: 10280006 ID: 406063 Release Date 11/21/08
12/01/08	130.0		-130.0		Forecast
12/01/08			0.0	130.0	W/O: 10280007 ID: 406064 Release Date 11/28/08
12/08/08	120.0		-120.0		Forecast
12/08/08			0.0	120.0	W/O: 10280008 ID: 406065 Release Date 12/05/08
12/15/08	110.0		-110.0		Forecast
12/15/08			0.0	110.0	W/O: 10280009 ID: 406066 Release Date 12/12/08
12/22/08	100.0		-100.0		Forecast
12/22/08			0.0	100.0	W/O: 10280010 ID: 406067 Release Date 12/19/08

Item Number: 01010
 Qty on Hand: 0.0
 Order Policy: PQQ
 Order Period: 7
 Order Qty: 0

Medical Ultrasound
 UM: EA
 Minimum Order: 0
 Maximum Order: 0
 Ord Mult: 0

BOM/Formula Code:
 Time Fence: 0
 Safety Time: 0
 Safety Stk: 0
 Yield%: 100.00%

Buyer/Planner:
 Supplier:
 Manufacturing Lead Time: 0
 Pur/Mfg: M Purchase LT: 0
 Inspect: No Inspect LT: 0
 Cumulative Lead Time: 0

Site: 10-100
 MRP Required: Yes
 Mstr Sched: Yes
 Plan Orders: Yes
 Issue Policy: Yes

Date	Gross Reqmt	Master Schedule	Projected Qty OH	Planned Order(Due)	Details
11/10/08	500.0		-500.0		SO: S0123456 Line: 1

Item Number: 01010
 Qty on Hand: 0.0
 Order Policy: PQQ
 Order Period: 7
 Order Qty: 0

Medical Ultrasound
 UM: EA
 Minimum Order: 0
 Maximum Order: 0
 Ord Mult: 0

BOM/Formula Code:
 Time Fence: 0
 Safety Time: 0
 Safety Stk: 0
 Yield%: 100.00%

Buyer/Planner:
 Supplier:
 Manufacturing Lead Time: 0
 Pur/Mfg: M Purchase LT: 0
 Inspect: No Inspect LT: 0
 Cumulative Lead Time: 0

Site: 10-100
 MRP Required: Yes
 Mstr Sched: Yes
 Plan Orders: Yes
 Issue Policy: Yes

End of Report

QAD Proprietary
MS-PR-225

Provides a printed copy of the information displayed in Master Schedule Detail Inquiry (22.21). While the data displayed are the same the selection criteria offered by the report is significantly enhanced over the inquiry.


Selective Materials Plan




Using Master Scheduling and RCCP



- ▲ Master Schedule Order Maintenance
- ▲ Master Schedule Order Browse/Report
- ▲ Sales Order Maintenance (Abnormal Demand)
- ▲ Seasonal Build Maintenance (optional)
- ▲ Seasonal Build Browse/Report (optional)
- ▲ Master Schedule Summary Inquiry/Report
- ▲ Master Schedule Detail Inquiry/Report
- ▲ Selective Materials Plan (optional)
- ▲ Item Resource Load Summary Inquiry/Report
- ▲ Item Resource Load Detail Inquiry/Report


Our Passion. Your Advantage.

Selective Materials Plan – Optional

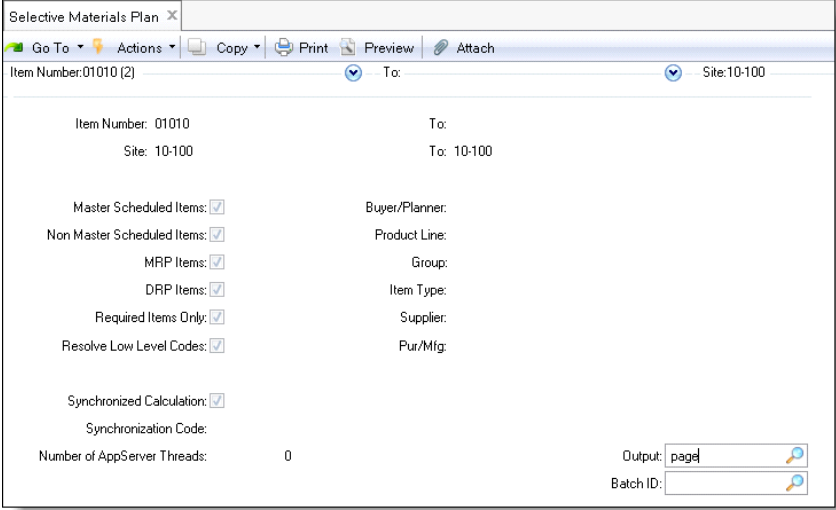

Selective Materials Plan (23.3)

QAD Proprietary
MS-PR-240

Selective Materials Plan (23.3) lets you plan master scheduled items separately from MRP items. If you use the computer-assisted approach to master scheduling, you may want to run Selective Materials Plan as follows:

- Run Selective Materials Plan for master scheduled items only
- Adjust the master schedule and rerun Selective Materials Plan as needed
- Run Selective Materials Plan for MRP-scheduled items only
- MRP provides time-phased balancing of:
 - Supply and demand for purchased and manufactured items
- MRP uses the master schedule and all other sources of demand and supply to:
 - Calculate gross requirements and projected on-hand inventory
 - Schedule and plan orders
 - Produce action messages for managing the materials plan
- Selective MRP runs as Net Change (MRP Required = Yes) or as Regenerative (MRP Required = No)
 - Plans only the items selected, passing down gross requirements to the next unselected level, but not replanning orders
 - Net Change Materials Plan (23.1) and Regenerate Materials Plan (23.2) items are based on low-level code, generating requirements at the top level first, then down through the structure one level at a time
- Selection can be based on:

- Item Number
- Site
- Buyer/Planner
- Prod Line
- Group
- Item Type
- Supplier
- Pur/Mfg
- One or both of the Master Scheduled Items or Non Master Scheduled Items flags must = Yes
 - The same is true of the MRP Items and DRP Items flags

Replanning Master Scheduled Items

When master scheduled items are selected, orders are planned for parent items and gross requirements are passed down to the next-level components and will not be replanned.

- No orders are planned for the components

Item Resource Load Summary Inquiry/Report



Using Master Scheduling and RCCP



- ▲ Master Schedule Order Maintenance
- ▲ Master Schedule Order Browse/Report
- ▲ Sales Order Maintenance (Abnormal Demand)
- ▲ Seasonal Build Maintenance (optional)
- ▲ Seasonal Build Browse/Report (optional)
- ▲ Master Schedule Summary Inquiry/Report
- ▲ Master Schedule Detail Inquiry/Report
- ▲ Selective Materials Plan (optional)
- ▲ **Item Resource Load Summary Inquiry/Report**
- ▲ Item Resource Load Detail Inquiry/Report

QAD
Our Passion. Your Advantage.

Item Resource Load Summary Inquiry

Item Resource Load Summary... X

Run Export to Excel View as PDF

Site: 10-100 Resource: UTS ASSY Start Date: 10/27/2010 End Date: Column Type: Week Per Column: 1 Columns: 12

Site: 10-100 Resource: UTS ASSY Ultrasound Assembly Unit of Measure:

Category	Past	10/27/2010	11/3/2010	11/10/2010	11/17/2010
Work Days	0	5	5	5	5
Capacity	0	365	365	365	365
Load	195.50	25	0	0	10.50
Capacity Less Load	-195.50	340	365	365	354.50
Cumulative	-195.50	144.50	509.50	874.50	1229.00

QAD Proprietary MS-PR-260

Calculating Load

Item Resource Load Inquiries (21.21) and Reports (21.22) can be run after the:

- Resource has been entered
- Conversion factor and lead times have been set up

QAD Enterprise Applications calculates the load automatically using the scheduled end-item quantities and the Resource Qty Per entered in Item Resource Bill Maintenance (21.17).

The Item Resource Load Summary displays the:

- Resource capacity
- Required resource capacity (production load) to meet scheduled production
 - In daily, weekly, or monthly buckets
- The load is subtracted from capacity
 - Over-capacity appears as a negative number in the Over/Under row
 - Under-capacity appears as a positive number

Cumulative Over/Under Load

The cumulative column displays the Over/Under quantity added to any over- or under-capacity from past planning periods.

Item Resource Load Summary Report

QAD
Our Passion. Your Advantage.

Item Resource Load Summary Report

Item Resource Load Summary... X

Go To Actions Copy Print Preview Attach

Site: 10-100 To: 10-100

Site: 10-100 To: 10-100

Resource: UTS ASSY To: UTS ASSY

Start Date: 10/26/2010

D/W/M/P: W

Per Column: 1

Under Cap %: 0.00%

Over Cap %: 0.00%

Output: |

Batch ID:

Item Resource Load Summary Report (21.22)

QAD Proprietary MS-PR-280

While the Item Resource Load Summary Report (21.22) shows the same information as Item Resource Load Summary Inquiry (21.21) it does allow selection based on a range of over/under percentage. This can be useful to filter out very small over/under loads to focus on the serious capacity issues.

For each resource, you can define resource bills (load profiles) that specify the amount of the resource required to manufacture a product line or item.

- Resource planning:
 - Evaluates the feasibility of production plans and master schedules
 - Identifies where adjustments are required

If the production plan needs more machine capacity, decrease production or increase machines. Catching the imbalance at this level allows adjustment of the plan before work is scheduled or customer promises are made.

Item Resource Load Detail Inquiry/Report



Using Master Scheduling and RCCP



- ▲ Master Schedule Order Maintenance
- ▲ Master Schedule Order Browse/Report
- ▲ Sales Order Maintenance (Abnormal Demand)
- ▲ Seasonal Build Maintenance (optional)
- ▲ Seasonal Build Browse/Report (optional)
- ▲ Master Schedule Summary Inquiry/Report
- ▲ Master Schedule Detail Inquiry/Report
- ▲ Selective Materials Plan (optional)
- ▲ Item Resource Load Summary Inquiry/Report
- ▲ Item Resource Load Detail Inquiry/Report

Item Resource Load Detail Inquiry

QAD
Our Passion. Your Advantage.

Item Resource Load Detail Inquiry

Item Resource Load Detail Inq X

Run Export to Excel View as PDF

Site: 10-100 Resource: UTS ASSY Start Date: 10/27/2010 End Date: Column Type: Week Per Column: 11 Columns: 12

Site: 10-100 Resource: UTS ASSY Ultrasound Assembly Unit of Measure: H

Category	Past	10/27/2010	11/3/2010	11/10/2010	11/17/2010
Work Days	0	5	5	5	5
Capacity	0	365	365	365	365
Load	195.50	25	0	0	10.50
Capacity Less Load	-195.50	340	365	365	354.50
Cumulative	-195.50	144.50	509.50	874.50	1229.00

QAD Proprietary MS-PR-300

The item resource load detail inquiry and report show the detail of the orders that are creating the load. In this example we see the work orders and items that are the specific labor load for this site. Once the summary has shown an overload condition exists, the master scheduler makes decisions about whether to schedule overtime, add extra shifts or reschedule the work orders. The detail reports will show the actual orders that may need to be rescheduled.

Item Resource Load Detail Report

Item Resource Load Detail Report												
10USA												
Past	10/27/10	11/03/10	11/10/10	11/17/10	11/24/10	12/01/10	12/08/10	12/15/10	12/22/10	12/29/10		
10/26/10	11/02/10	11/09/10	11/16/10	11/23/10	11/30/10	12/07/10	12/14/10	12/21/10	12/28/10	01/04/11		
W/O: 08020017	4	0	0	0	0	0	0	0	0	0	0	0
W/O: 08020018	4	0	0	0	0	0	0	0	0	0	0	0
W/O: 08020019	4	0	0	0	0	0	0	0	0	0	0	0
W/O: 08020020	4	0	0	0	0	0	0	0	0	0	0	0
W/O: 08020021	4	0	0	0	0	0	0	0	0	0	0	0
W/O: 08020022	4	0	0	0	0	0	0	0	0	0	0	0
W/O: 08020023	4	0	0	0	0	0	0	0	0	0	0	0
W/O: 08020024	4	0	0	0	0	0	0	0	0	0	0	0
W/O: 08020025	4	0	0	0	0	0	0	0	0	0	0	0
W/O: 08020026	4	0	0	0	0	0	0	0	0	0	0	0
Total Load	196	25	0	0	11	0	0	6	0	0		
Over/Under	-123	340	365	365	355	365	365	365	359	365	292	
Cumulative	-123	217	582	947	1,302	1,667	2,032	2,397	2,756	3,121	3,413	


While the data displayed are the same for the inquiry and report, some schedulers will prefer the format of the report, which can be viewed on the monitor or printed.

Exercise: Processing

Review a Seasonal Build Forecast

This activity covers entering and reviewing a forecast and a seasonal build plan.

- Item 01042 at site 10-100 is being introduced into a new marketplace 4 weeks from next Monday.

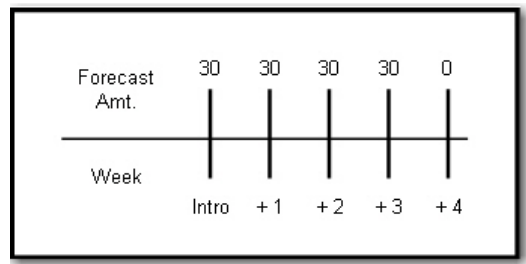

- As a hedge against sales being greater than anticipated, you would like to have an additional 60 units in stock available on the date of the introduction. These will be produced in the two weeks prior to the introduction.

Use Seasonal Build Maintenance (22.9) to enter a seasonal build schedule using Monday dates.

Field	First Entry	Second Entry	Third Entry
Site	10-100	10-100	10-100
Item Number	01042	01042	01042
Date	[2 wks prior]	[1 wk prior]	[Intro Date]
Reference	Intro	Intro	Intro
Seasonal Inventory	30.0	60.0	0.0

- Run a Seasonal Build Inquiry for item 01042 to ensure that the data has been entered correctly.
- Run Selective Materials Plan (23.3) for item 01042.
- Review the Master Schedule Summary Inquiry (22.18) and Master Schedule Detail Inquiry (22.21) to review the impact of the seasonal build.

Rough-Cut Capacity Planning

In this activity, you will level a load using the rough-cut capacity planning (RCCP) process. The activity includes creating master scheduled orders, running selective MRP, reviewing inquiries and reports, and increasing capacity to balance the load. Use item 01041, site 10-100 throughout the activity.

- Use Master Schedule Order Maintenance (22.13) to create a work order.

Field	Data
Work Order	[blank]
ID	[blank]
Item Number	01041

Field	Data
Type	[blank]
Site	10-100
Qty Ordered	100
Order Date	[Today's Date]
Release Date	[Two weeks from today]
Due Date	[Three weeks from today]

- 2 Run Selective Materials Plan (23.3) for item 01041 at site 10-100.
- 3 Use Item Resource Load Summary Inquiry (21.21) to review the resource load for site 10-100, resource Labor. Is there enough capacity to do the plan?
- 4 Using Resource Maintenance (21.1), increase labor capacity for site 10-100. How much do you need to increase the daily labor supply?

Field	Data
Resource	Labor
Site	10-100
Reference	Normal
Cap/Day	150

- 5 Use Item Resource Load Summary Inquiry (21.21) and Item Resource Load Detail Inquiry (21.23) to review the effects of your changes.

Course Summary



Course Overview

- ✓ Introduction to Master Scheduling and RCCP
- ✓ Business Considerations
- ✓ Set up Master Scheduling and RCCP
- ✓ Use Master Scheduling and RCCP

Appendix A

Workshops and Study Questions

Master Schedule Setup

- 1 Explain what fields must be set to have forecast consumption occur.

- 2 In QAD Enterprise Applications, to allow shipment of seasonal build requirements, what entry must be entered on the Seasonal Build Maintenance screen?

- 3 What fields in Item-Site Planning Maintenance are used to designate a master schedule item?

- 4 A forecast is considered to be a dependent demand requirement.
True/False
- 5 Abnormal demand is the preferred method of building to inventory.
True/False
- 6 A Plan Orders flag setting of No constitutes the fully manual approach to master scheduling.
True/False
- 7 A time fence is the longest period of time it takes to either purchase or manufacture an item, assuming nothing is on hand.
True/False
- 8 Available-to-promise (ATP) is a manually entered value in QAD Enterprise Applications.
True/False
- 9 Dependent demand items can be shipped on a sales order.
True/False
- 10 In any time period, the ATP quantity can never be less than the projected on-hand quantity.
True/False

RCCP

- 1 List four of the key resources for scheduled end items in your company's plants.
 - a
 - b
 - c
 - d

- 2 If the Item Resource Summary shows 150% load in each of the next four weeks, what do you need to do?

- 3 The item resource plan does not take into account component production demands.
TrueFalse
- 4 A resource plan that appears slightly over or under capacity is typically ignored.
TrueFalse
- 5 Item resource loads are calculated from _____.
- 6 Overtime is scheduled by entering a Reference and a positive number of hours in Item Resource Bill Maintenance.
TrueFalse
- 7 Rough-cut capacity planning only looks at firm planned work orders and repetitive schedules.
TrueFalse
- 8 A negative lead time offset in the Item Resource Bill Maintenance indicates that the resource is needed before/after production begins.
BeforeAfter

Answers to Master Schedule Setup Study Questions

- 1 Set Consume Forecast = Yes on the sales order and enter a positive value in Consume Fwd and/or Consume Back in Sales Order Control.
- 2 A quantity smaller than the previous seasonal build entry must be entered. To release the entire seasonal build quantity, enter a zero.
- 3 In fact, an item is a master schedule item if the planner says it is. The planner determines whether it should be selected during a selective MRP based on Master Schedule = Yes or No. The planner also decides whether the system should create planned orders.

Set the following fields: Master Sched = Yes, Plan Orders = No. The key is the Plan Orders setting, which tells MRP whether to plan the item or not. You can set Plan Orders = Yes, and then use a Time Fence value to control the creation of orders within the near term horizon.
- 4 False. Forecasts and sales orders are independent demand requirements.
- 5 False. Seasonal build is the accepted method of building to inventory.
- 6 True.
- 7 False. A time fence is a period of calendar days from the system date for which MRP will not create planned orders.
- 8 False. ATP is calculated by the system and appears on the Master Schedule Summary Inquiry screen.
- 9 True.
- 10 False. If ATP is negative, it is over-promised for the remaining planning horizon.

Answers to RCCP Study Questions

- 2 Reduce production by 50% or increase capacity by 50%.
- 3 True. The Capacity Requirements Plan performs this task.
- 4 True. Slight deviations can usually be worked out on the shop floor.
- 5
 - a The production forecast from the Product Line Plan.
 - b The master schedule for the items.
- 6 False. Use Resource Maintenance.
- 7 False. It includes released, firm planned, exploded, and allocated orders.
- 8 After.

Appendix B

Reports, Inquiries, Browsers

**Master Scheduling and RCCP
Reports, Inquiries, Browsers**

Report, Inquiry, Browse	Function/Purpose
Forecast Inquiry	Displays forecasts for any item or product subject to independent demand. Forecasts may also be displayed for spares requirement, planning items and configured products.
Forecast Report	Provides a means of printing the information displayed in Forecast Inquiry.
Seasonal Build Inquiry	Displays seasonal build forecasts which are usually derived from a product line plan, then used to develop the operations plan and the master production schedule. They are then periodically adjusted based on actual results or changes in the business plan.
Seasonal Build Report	Provides a means of printing the information displayed in Seasonal Build Inquiry.
Master Schedule Order Inquiry	Displays information about master schedule orders which determine how items will be made (routing), and what components will be used (BOM).
Master Schedule Order Report	Provides a means of printing the information displayed in Master Schedule Order Inquiry.
Master Schedule Summary Inquiry	Displays vital information derived from the production forecast, sales orders, gross requirements, master scheduled receipts, projected quantities on hand. Projection by period of the on-hand balance plus incoming orders minus the requirements
Master Schedule Summary Report	Provides a means of printing the information displayed in Master Schedule Summary Inquiry.
Master Schedule Detail Inquiry	The Master Schedule Detail Inquiry and Report functions 22.21 and 22.22 display the same information as the Master Schedule Summary Inquiry and Report, sequenced by due date. They also include source-to-demand pegging details, allowing you to identify the actual work order or sales order generating a particular item requirement.
Master Schedule Detail Report	Provides a means of printing the information displayed in Master Schedule Detail Inquiry.
Item Resource Bill Inquiry	Displays information on resource requirements for individual items.
Item Resource Bill Report	Provides a means of printing the information displayed in Item Resource Bill Inquiry
Item Resource Load Summary Inquiry	Displays the required resource capacity (production load) to meet scheduled production in daily, weekly, or monthly buckets. The load is subtracted from capacity: over-capacity appears as a negative number in the Over/Under row, under-capacity appears as a positive number.
Item Resource Load Summary Report	Provides a means of printing the information displayed in Item Resource Load Summary Inquiry.
Item Resource Load Detail Inquiry	Displays detailed information about the required resource capacity.
Item Resource Load Detail Report	Provides a means of printing the information displayed in Item Resource Load Detail Inquiry.
